



Newmont Corporation
Cripple Creek & Victor Gold Mining Company
100 North 3rd St
P.O. Box 191
Victor, CO 80860
www.newmont.com

January 27, 2022

ELECTRONIC DELIVERY

Mr. Elliott Russell
Environmental Protection Specialist
Colorado Department of Natural Resources
Division of Reclamation, Mining and Safety
Office of Mined Land Reclamation
1313 Sherman Street, Room 215
Denver, Colorado 80203


**RE: Permit No. M-1980-244; Cripple Creek & Victor Gold Mining Company; Cresson Project;
Schist Island Backfill Weekly Report**

Mr. Russell,

In accordance with Amendment Thirteen Second Adequacy Review Response, comment number 73; Newmont Corporation's Cripple Creek and Victor Gold Mining Company (CC&V) hereby provides a weekly report documenting backfilling activities completed in Schist Island during Week 20 of the project, covering the period from 1/08/22 to 1/14/22.

Should you require further information please do not hesitate to contact Katie Blake at 719-689-4048 or Katie.Blake@Newmont.com or Justin.Raglin@Newmont.com.

Regards,

DocuSigned by:

A5AA058117F54C4...

Justin Raglin
Sustainability & External Relations Manager
Cripple Creek and Victor Gold Mining Company

EC: E. Russell – DRMS
M. Cunningham – DRMS
M. Crepeau – Teller County
L. Morgan – Teller County
J. Raglin – CC&V
K. Blake – CC&V
M. Bujenovic – CC&V
N. Townley – CC&V

Enc (1)

WE2022.01.14 VLF2 Phase 3 Weekly Report_week 20

File: S:\CrippleCreek\na.cc.admin\Environmental\New File Structure\2-Correspondence\DNR\DRMS\2021\Outgoing

ATTACHMENT 1

Newmont Mining Corporation
 Cripple Creek & Victor Gold Mine
 VLF2 Phase 3 Site Support 2022
 NewFields Job No. 475.0106.053
 Week Ending Friday, January 14, 2022



FIELD WEEKLY PROGRESS REPORT

PROJECT: VALLEY LEACH FACILITY (VLF2) PHASE 3 CQA HIGH COMPACTION BACKFILL
SITE: CRIPPLE CREEK & VICTOR GOLD MINE (COLORADO)
CONTRACTOR: NEWMONT CC&V MINING OPERATIONS
WEEK ENDING: FRIDAY, JANUARY 14, 2022

REPORTING PERIOD: 01.08.2022 THROUGH 01.14.2022

Days	Sat	Sun	Mon	Tue	Wed	Thu	Fri
Work Shifts	D/N	D/N	D/N	D/N	D/N	D/N	D/N
D – DAYSHIFT		N – NIGHTSHIFT			W – WEATHER		

AMBIENT TEMPERATURE RANGES:

HIGHS: 49°F TO 31°F

LOWS: 30°F TO 8°F

WEATHER CONDITIONS:

CLOUD COVER: PARTLY TO MOSTLY CLOUDY

PRECIPITATION: SNOW 01/14/2022 (TRACE)

WIND: WIND GUSTS FROM 10 TO 55 MPH

NEWFIELDS PERSONNEL ONSITE:

Personnel	Sat	Sun	Mon	Tue	Wed	Thu	Fri
	Jan 8	Jan 9	Jan 10	Jan 11	Jan 12	Jan 13	Jan 14
Jay Moore	-	-	-	-	-	-	-
Tyler Wendlandt	-	LS	LS	LS	LS	LS	LS
George Fry	-	-	-	-	-	-	-
PR – Project Resident; LS – Lead Soils Technician; LG – Lead Geosynthetics; ST – Soils Technician; GT – Geosynthetics Technician; LT – Laboratory Technician; PCE – Project Certifying Engineer							

1.0 MINING OPERATIONS

1.1 Schist Island High Compaction Back Fill

CC&V completed the placement of the 9975' elevation high compaction backfill lift. CC&V began the placement of the 9980' elevation high compaction backfill lift. Run of Mine material was loaded from the Schist Island Pit and West/South Cresson Pit and hauled by 793 haul trucks to the high compaction backfill. A D10 dozer placed material in a 5 foot GPS controlled leading edge lift. The haulage traffic travelled over the entirety of the fill, splitting tracks with each loaded haul



truck. The D10 leveled out the windrows along the pit wall and pushed structural material into any surface irregularities along the pit wall.

CC&V shovel and loader operators monitored the Run of Mine material size being sent to the high compaction backfill. Out of specification loads containing 2 foot plus sized material were sent to the ECOSA stockpile. 2 foot plus sized material that was not removed at the dig-face by the shovel or loader operators was removed by a D10 dozer during material placement. The oversize material was stockpiled by the dozer out of the way above the current lift on the haul road against the pit high wall. A 993 loader loaded a 777 haul truck with the unsuitable material and it was then hauled to the ECOSA stockpile.

Contour grading continued in the floor of the PSSA. A D10 dozer graded overburden backfill material to the edges of the backfill placement for future removal from the bottom of the pond.

2.0 MEETINGS AND COMMUNICATIONS

NewFields personnel met with Mine Operations Supervision about the high compaction backfill progress and material quality.

3.0 MISCELLANEOUS, ISSUES, AND CONCERNS

- NewFields personnel completed the approval of the 9975' lift. Visual inspection and the method compaction specification were utilized to approve the lift.
- NewFields personnel approved a section of the 9980' lift. Visual inspection and the method compaction specification were utilized to approve the lift.
- A progress map provided by Newmont CC&V was utilized to create the attached figures showing high compaction backfill progress.



4.0 PHOTOGRAPHS



January 11, 2022 – High Compaction Backfill placement (TW)



January 12, 2022 – High Compaction Backfill placement (TW)

Newmont Mining Corporation
 Cripple Creek & Victor Gold Mine
 VLF2 Phase 3 Site Support 2022
 NewFields Job No. 475.0106.053
 Week Ending Friday, January 14, 2022



January 14, 2022 – High Compaction Backfill progress (TW)

Report Review and Approval:

Role	Name	Signature
CQA Monitor/Report Prepared By	Tyler Wendlandt	
<i>Or CQA Designee</i>		
Project Engineer	Jeff Gaul	DocuSigned by:  1122B343C4A54DD...
<i>Or Projects Designee</i>		


Newmont Mining Corporation
Cripple Creek & Victor Gold Mine
VLF2 Phase 3 Site Support 2022
NewFields Job No. 475.0106.053
Week Ending Friday, January 14, 2022



Attachments:

Figure 1 – Section Approval Progress 9975' Lift (Map Date 01/06/22)

Figure 2 – Section Approval Progress 9980' Lift (Map Date 01/13/22)

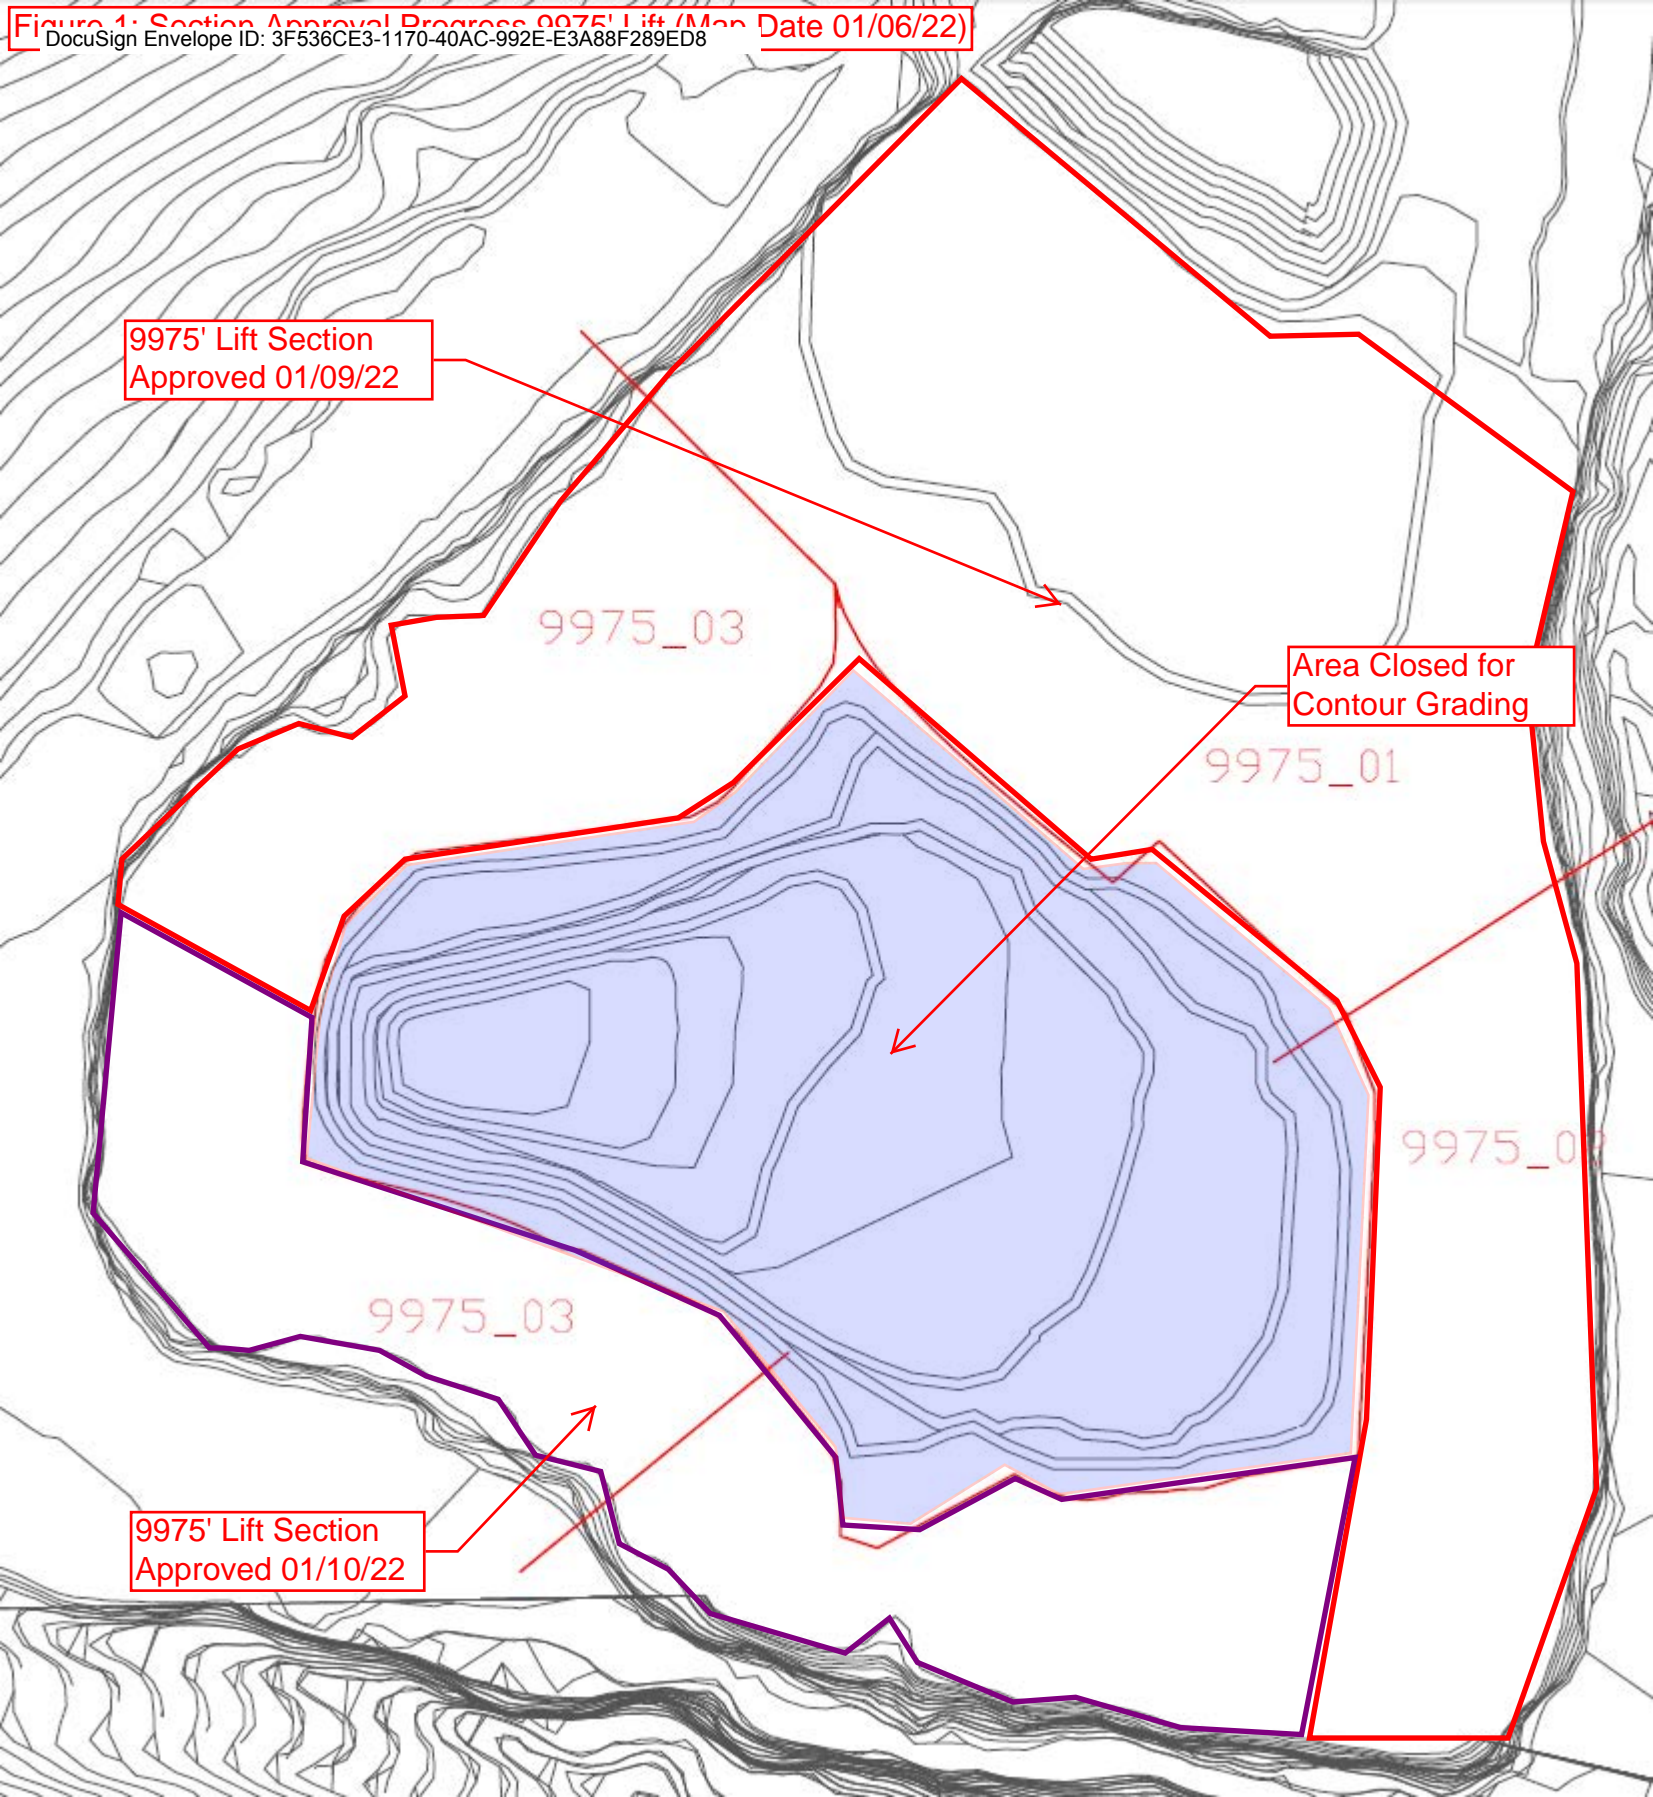

9980' Lift Section
Approved 01/13/22

9980_01

9980_01

Area Closed For
Contour Grading

~~9980_02~~

9980_02

01.13.2022 9980'
Lift Progress
