



CC&V Action Plan - VLF2 Phase 3A

Johnna Gonzalez <Johnna.Gonzalez@newmont.com>

Tue, Feb 27, 2024 at 7:19 AM

To: "Elliott Russell (DNR-DRMS)" <elliott.russell@state.co.us>

Cc: "Means - DNR, Russ" <russ.means@state.co.us>, Amy Eschberger - DNR <amy.eschberger@state.co.us>, Katie Blake <Katie.Blake@newmont.com>, Nikie Gagnon - DNR <nikie.gagnon@state.co.us>

Hi Elliott,

Please see the attached PowerPoint presentation regarding CC&V's Action Plan for the remediation on Phase 3A. Also included in the presentation is the acreage for the exclusion zone area.

A weekly progress report will be submitted to DRMS on Tuesdays for the week prior activities.

If you have any additional questions, please let me know.

Thanks,



Johnna Gonzalez

ENVIRONMENTAL

100 N 3rd Street
PO Box 191

Victor, CO 80860

M 719.313.0447

NEWMONT.COM

From: Elliott Russell (DNR-DRMS) <elliott.russell@state.co.us>

Sent: Thursday, February 15, 2024 3:51 PM

To: Katie Blake <Katie.Blake@Newmont.com>

Cc: Johnna Gonzalez <Johnna.Gonzalez@newmont.com>; Means - DNR, Russ <russ.means@state.co.us>; Amy Eschberger - DNR <amy.eschberger@state.co.us>; Nikie Gagnon - DNR <nikie.gagnon@state.co.us>; Jeff Fugate <Jeff.Fugate@coag.gov>

Subject: [EXTERNAL] RTB Letter and Notice of Board Hearing M1980244

Katie,

As discussed in yesterday's meeting, here is the Reason to Believe (RTB) a Violation Exists and Notice of Board Hearing regarding the VLF2 Phase 3 ore stacking issue. The matter has been scheduled before the MLRB on March 20th. This notice was sent via certified mail today to Lori Smith.

Please let me know if you have any questions.

Elliott Russell

Environmental Protection Specialist

Minerals Regulatory Program



I am working remotely and can be reached at 303.903.4456

*****Please note the Division's mailing address has changed*****

P 303.866.3567 x8132 | F 303.832.8106 | C 303.903.4456

Physical: 1313 Sherman Street, Room 215, Denver, CO 80203

Mailing: DRMS Room 215, 1001 E 62nd Ave, Denver, CO 80216

Elliott.Russell@state.co.us | <https://drms.colorado.gov>


 **Newmont CC&V VLF2P3A Cell 5 work plan 02262024.pptx**
6111K



Cripple Creek and Victor Mine VLF 2 Phase 3A Work Plan


26TH FEBRUARY 2024

VLF 2 Phase 3A 10050 Lift – February 5, 2024 Status

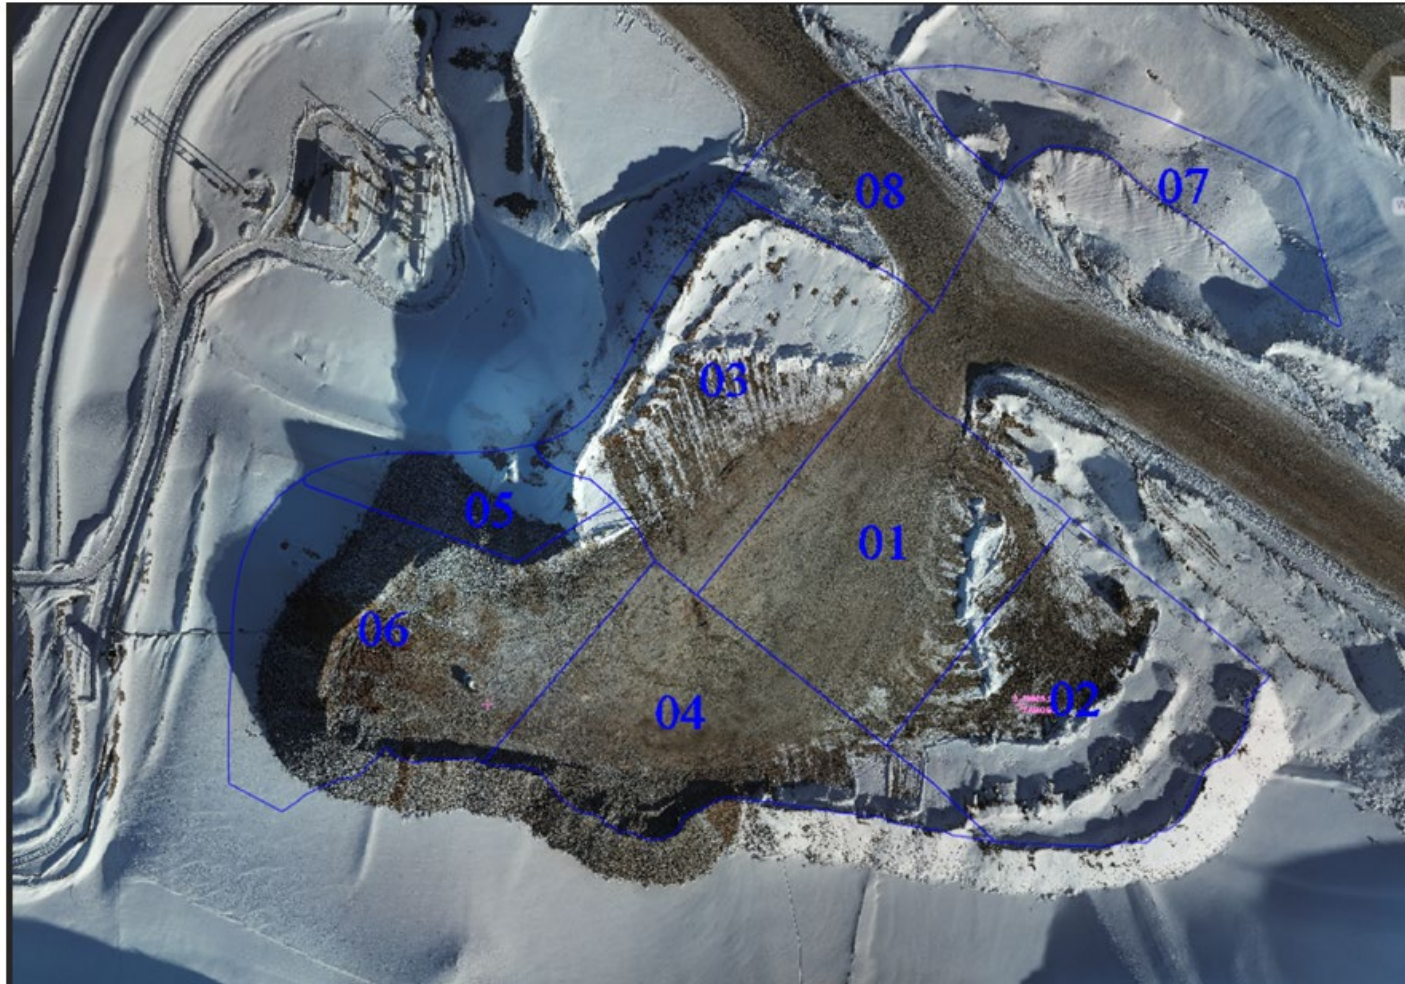


Drone photo
and scan of
10050 lift,
Cell 5 and
Cell 6

Limits of No Leaching – Piping Detail


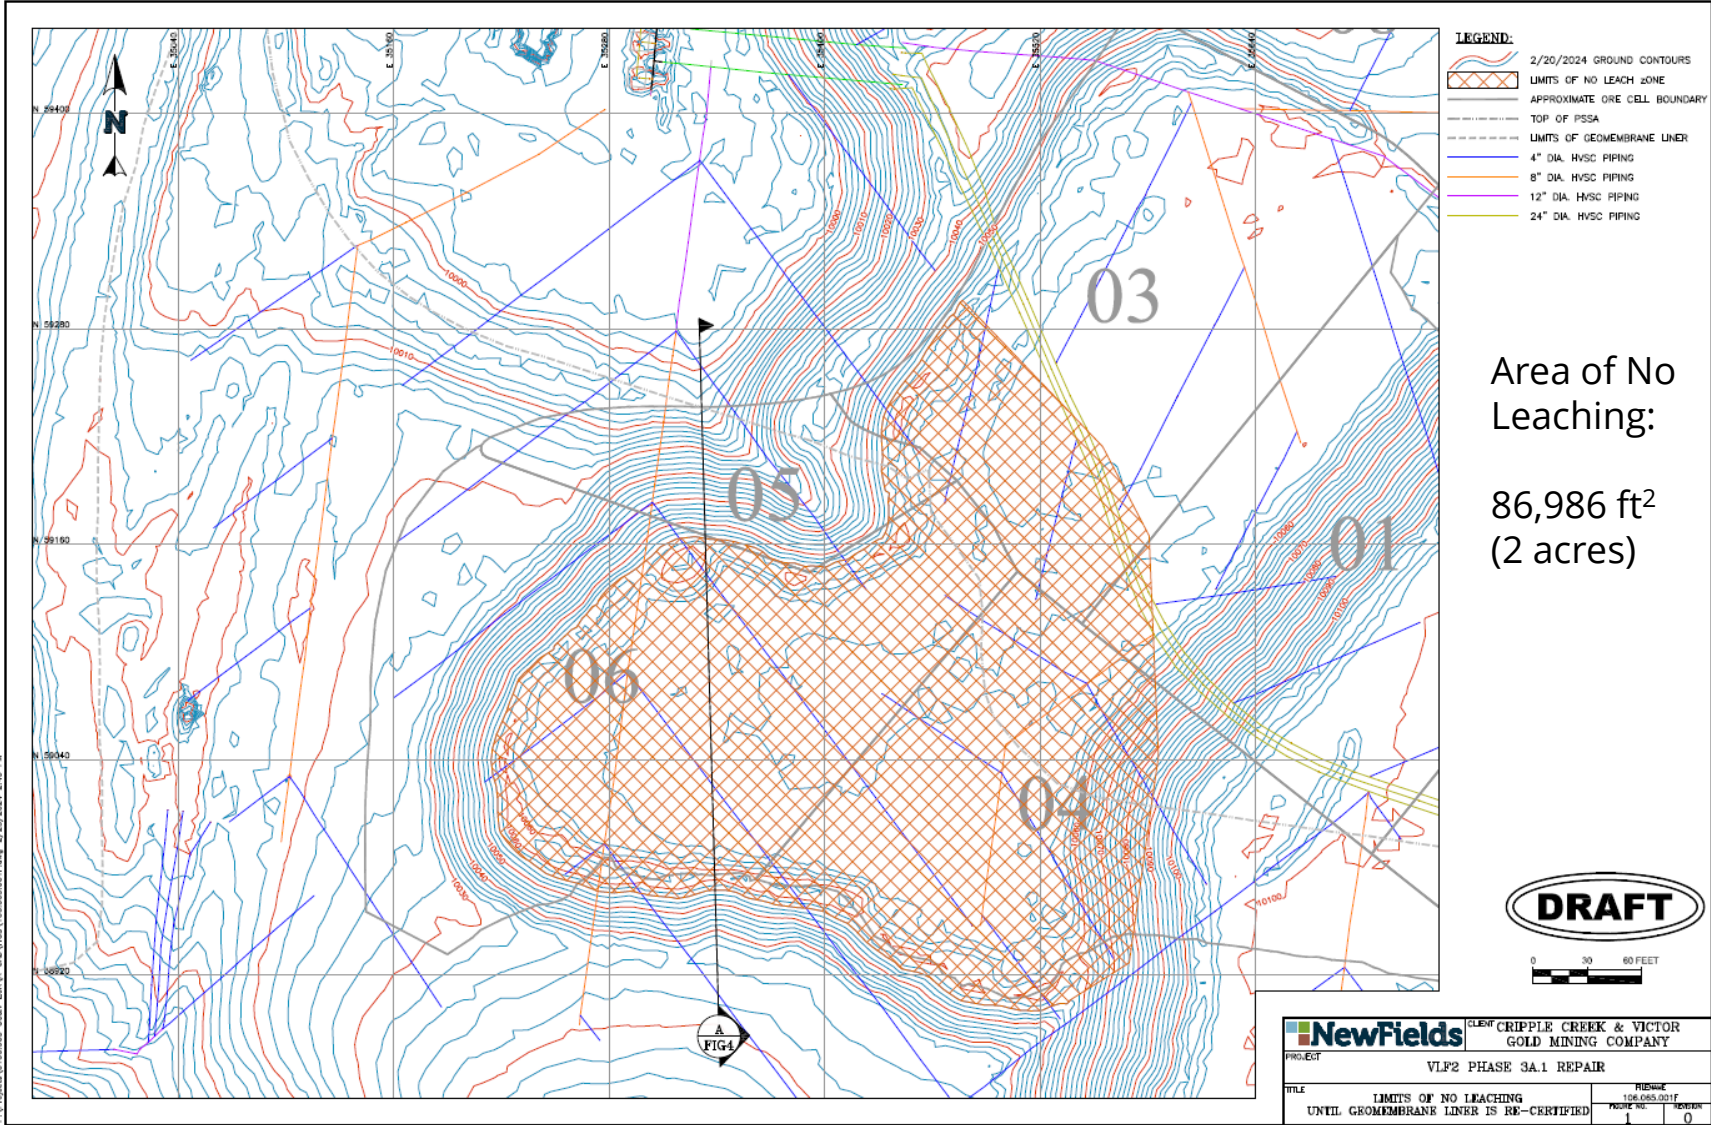


Limits of Excavation

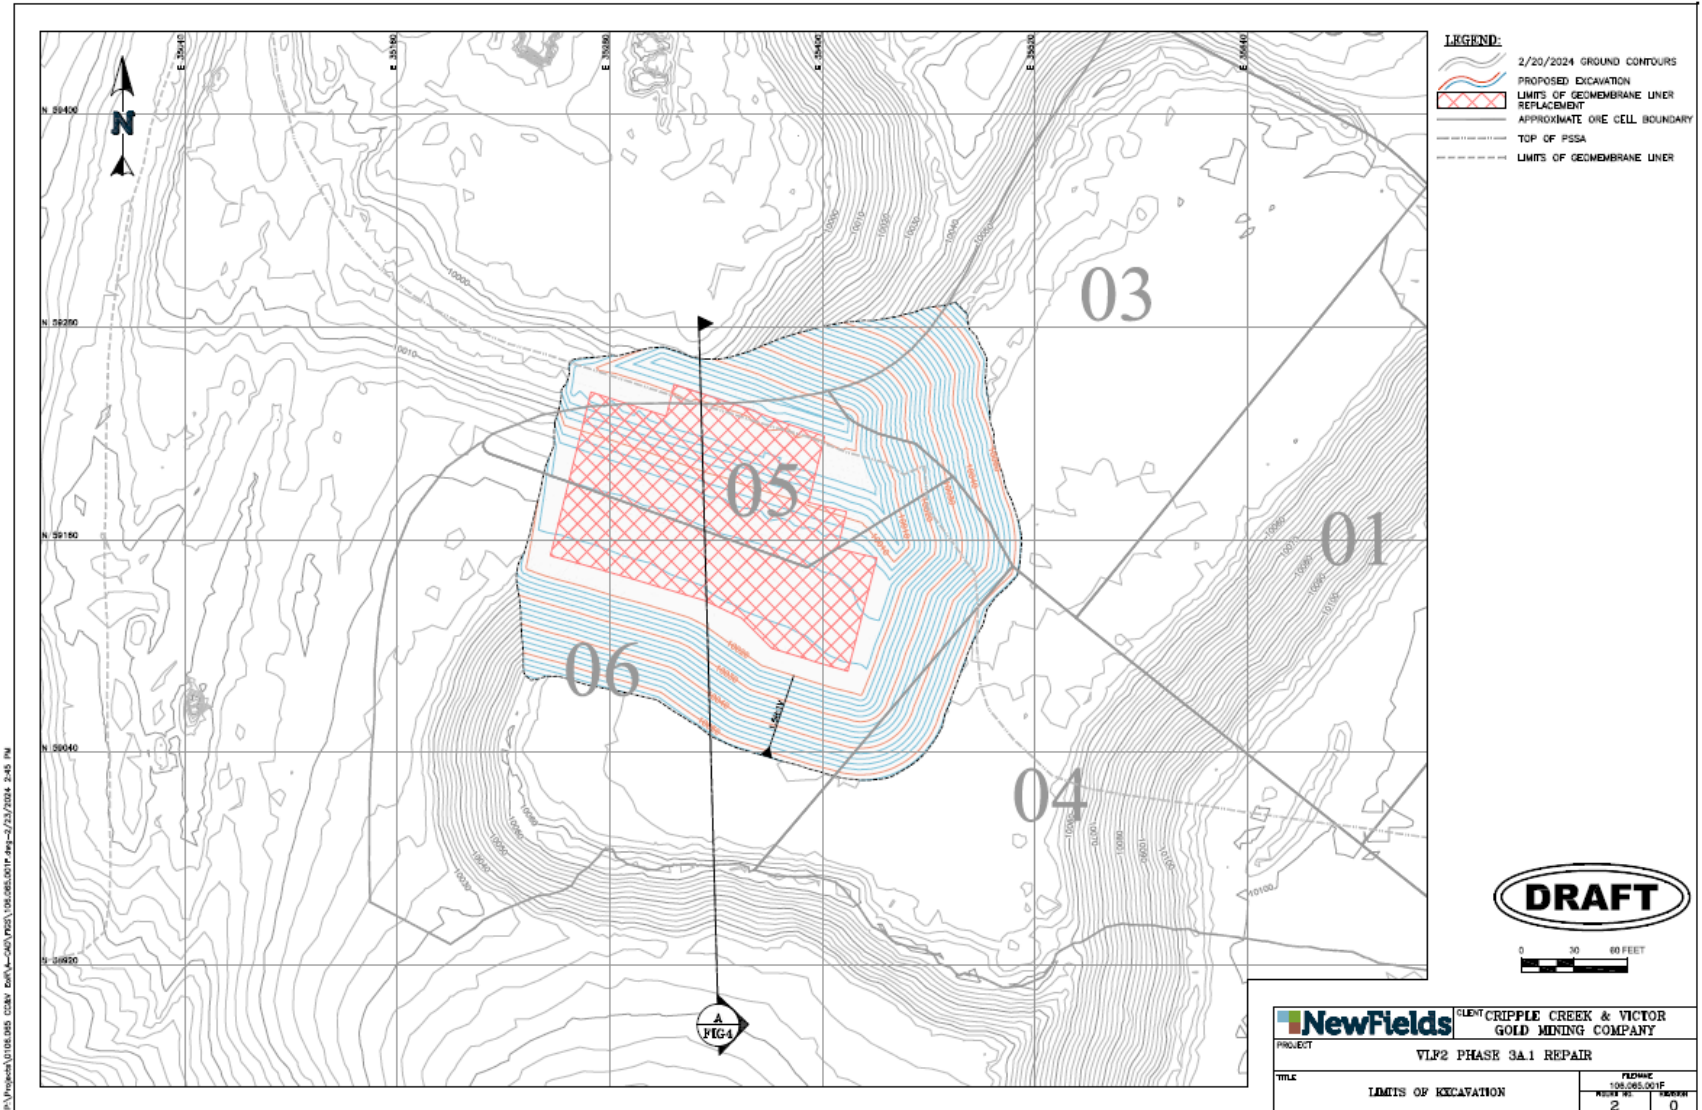

J:\Projects\0105.065.001F CRIPPLE CREEK & VICTOR GOLD MINING COMPANY\0105.065.001F.dwg - 2/12/2024 2:45 PM


Cross Section

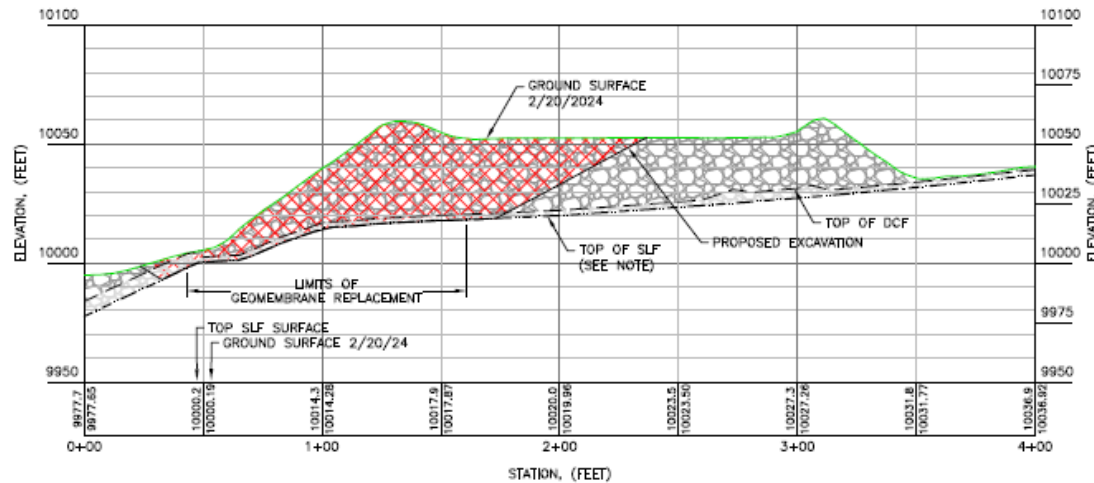

DRAFT

NewFields		CLIENT CRIPPLE CREEK & VICTOR GOLD MINING COMPANY	
PROJECT		VLP2 PHASE 3A.1 REPAIR	
TITLE		SECTION	
PROJECT NO.		106-000-0011F	
PAGE NO.		4	
REVISION		0	

Limits of Geomembrane Replacement, Liner Type

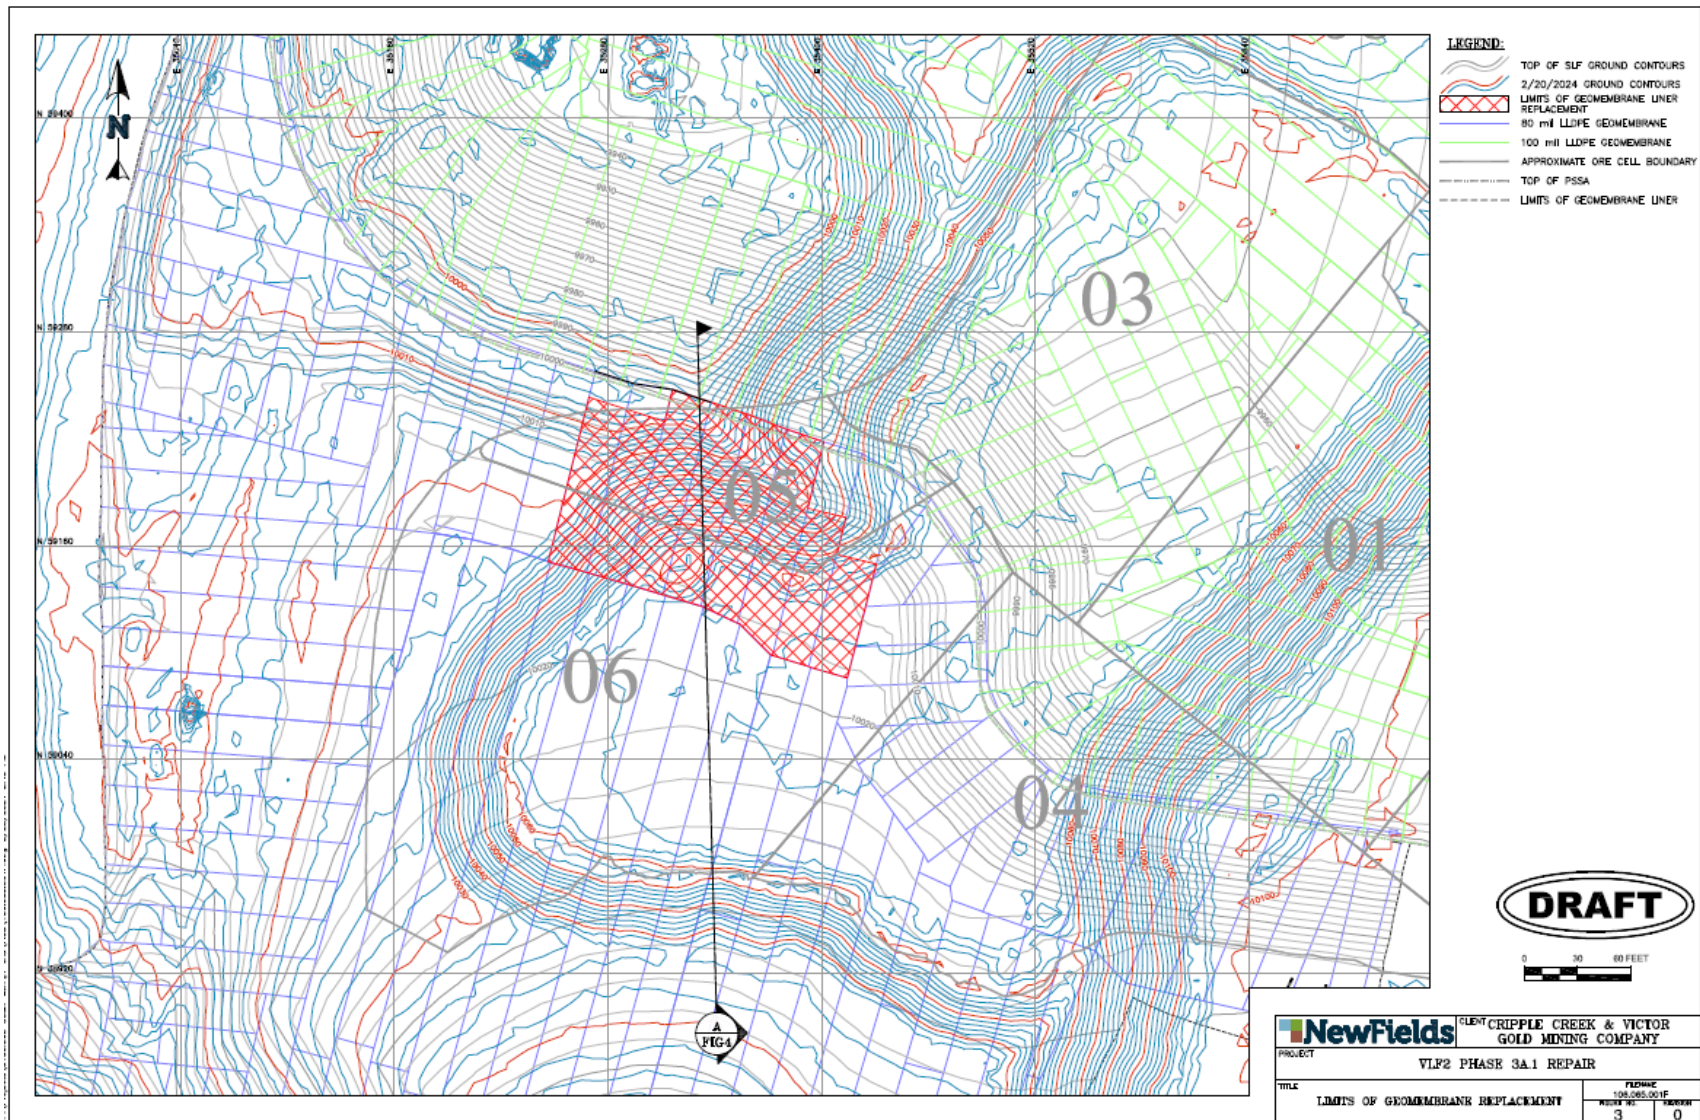

Project Schedule



Task	Duration	Who	February				March				April				
			5	12	19	26	4	11	18	25	1	8	15	22	29
VLF2 Phase 3 Repair															
Define Excavation Area		NewFields													
Develop Plan		All													
DRMS Review		S&ER													
Survey Layout		MTS													
Bulk Material Move (5 ft above liner)	1 week	Mine Ops													
Mobilization	1 week	JHL													
Dozer push to Mine Ops (2 ft above liner)	0.5 week	JHL													
Expose Liner with Mini Excavator	2-3 weeks	JHL													
Repair Liner	?	TBD													
Replace DCF	0.5 week	JHL													
North Road	0.5 week	JHL - Conley													
Survey for RoC		FSW													
Record of Construction Documentation		NewFields													
DRMS Review		S&ER													
Manage Repair		Mine Ops													


Old Controls: Stacking Order Guidance 10050 Lift



VLF 2 Stacking Plan – Phase 3A

Stack Order

10050_002 ->
10050_003 ->
10050_004 ->
10050_005 (crushed only) ->
10050_006 ->
10050_007 ->

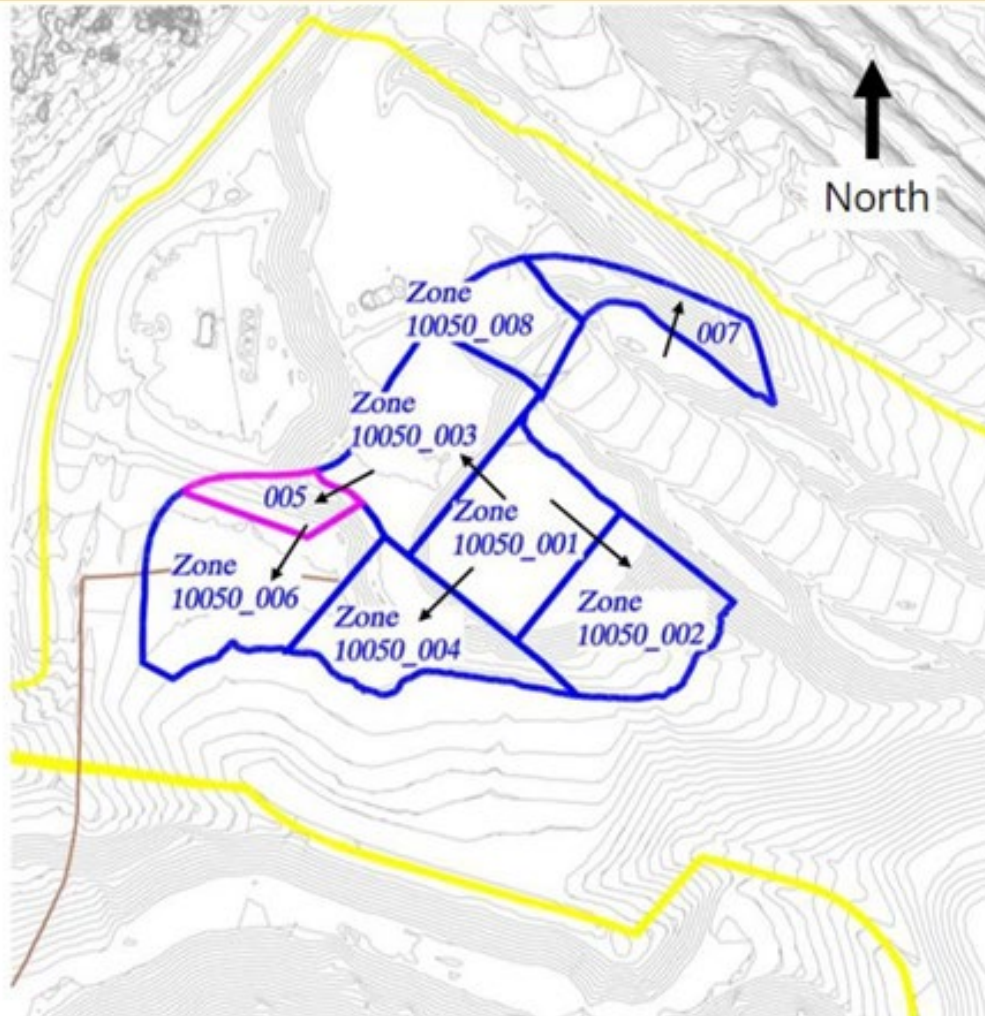

Blue boundary is an all material types zone.

Magenta is crushed only

Arrows show stacking direction.

Dumping Order and Cell information given in planning packet.

- Electronic and paper copies available
- Foreperson uses this information to line out the crews during the shift

New Controls: Stacking Order Guidance 10100 Lift




VLF 2 Stacking Plan – Phase 3A

Stack Order

10100_007->
10100_008->
10100_009->
10100_010->
10100_011->

- Stacking order must be strictly followed.
- Overflows goes to VLF 2 10300
- Contact STP if you face any stacking challenges

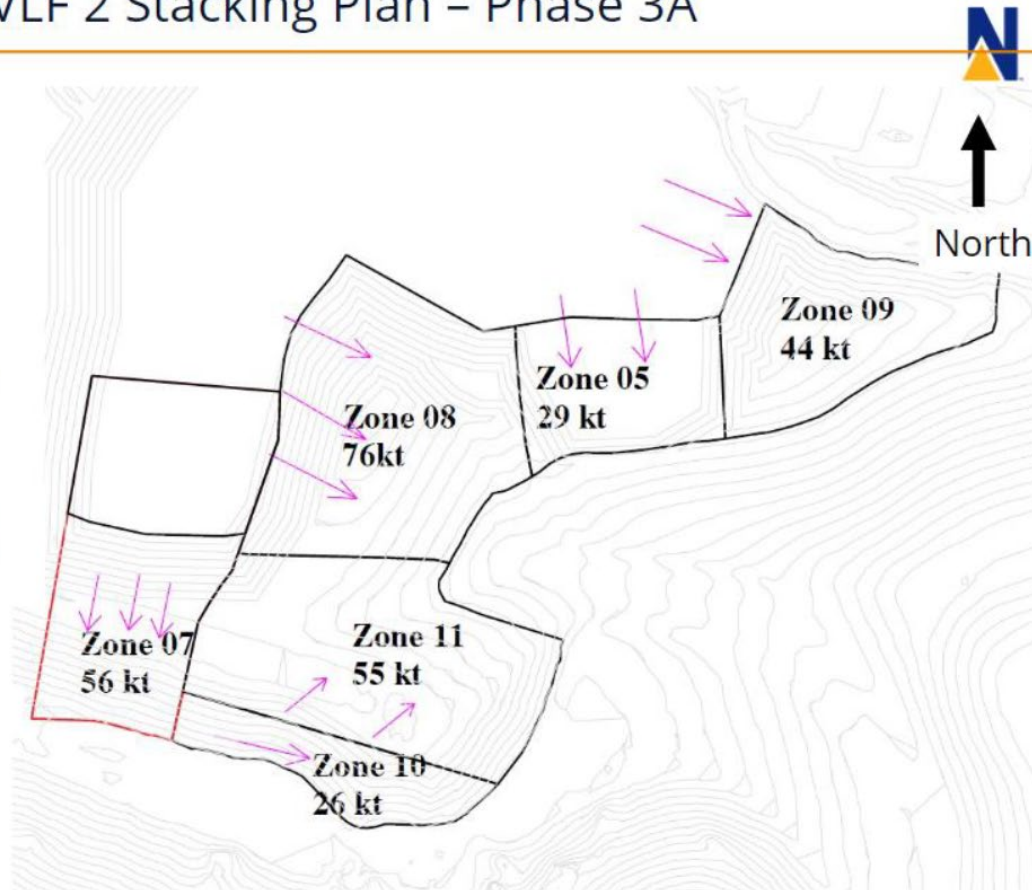

More details added:

- Instructions
- Directions
- Communication with operators

New Controls for Stacking Guidance: Minestar Files

