



OWL MOUNTAIN PARTNERSHIP

P.O. Box 737

Walden Colorado 80480

November 25, 2019

Colorado Water Conservation Board
1313 Sherman Street
Room 718
Denver, Colorado 80203

FINAL REPORT

Reference Purchase Order: POGGI,PDAA,202000002425

Dear CWCB:

The "Squibob Ditch" project has been completed. The project consisted of the installation of a check structure in the Squibob ditch which allows the producer to control the amount of water exiting onto the field. RLW Enterprises welded the structure and performed the installation.

No major obstacles were encountered with the installation of the project.

The proposed budget is identical to the actual budget.

The Natural Resources Conservation Service (NRCS) certified the structure. The check structure met NRCS's Standards and Specifications for Structures for Water Control #587. NRCS approved the matching payment amount of \$7,109.64. The landowner contribution is \$899.36.

Therefore, we are requesting a final payment of \$8,640: \$8,001 from CWCB's WSRF to cover the remaining cost of installation and \$640 for Owl Mountain Partnership's 8% administration fee.

Sincerely,

Kendall E. Ray

Administrator for Owl Mountain Partnership

Baller Ranch LLC. Structure For Water Control Squibob Ditch

Purchase Order Number: POGG1,PDAA, 202000002425



Practice Certification


***Practice is complete and all materials and installation meet
NRCS Specification #587 - Structure For Water Control.***

Debbi Heeney

**NRCS District Conservationist
100 Main Street
Walden, Colorado 80480
Phone: (970)723-4724**

USDA Natural Resources Conservation Service
Colorado

United States Department of Agriculture

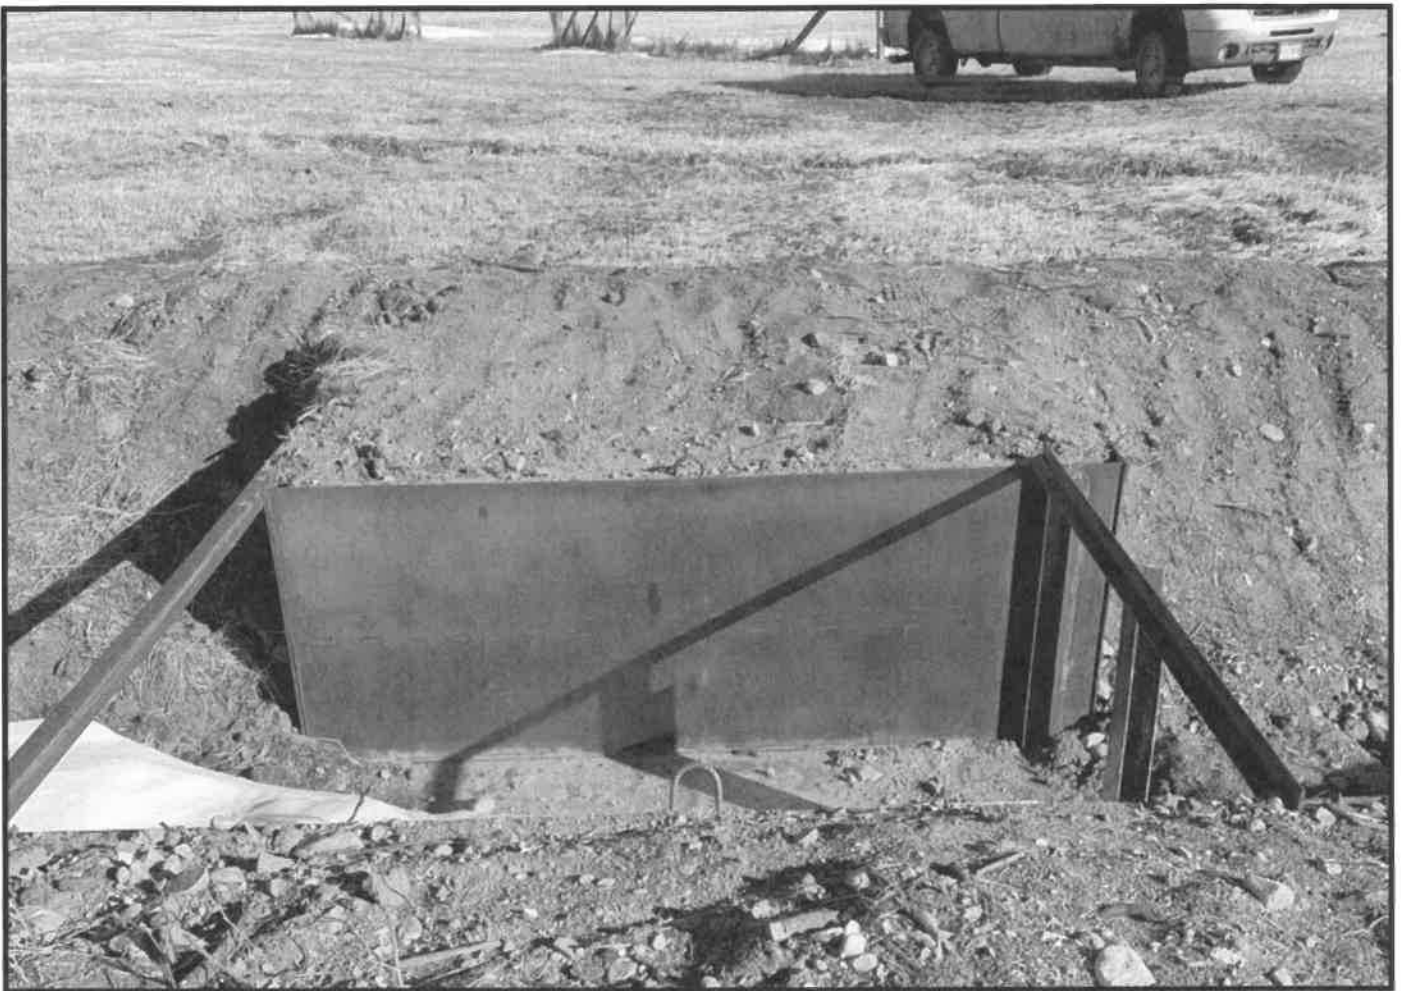

Photos of backfilled structure. 1/4" steel walls and floor with 1/4" x 2" x 2" angle iron reinforcement and check board slots. Dimensions and elevations are as designed. Welds and construction are good. Compaction is present and installation is good. Anodes are in place - (2) 32lb.

