

Table 1. Construction Activity Dates for Monitoring Wells

Well ID	Date Borehole Collared	Date Borehole TD	Date Well Completed	Final Development Date
MW13	8/11/2012	8/18/2012	9/7/2012	9/9/2012
MW14	8/20/2012	8/22/2012	9/4/2012	9/15/2012
MW15	9/13/2012	10/15/2012	11/3/2012	11/4/2012
MW16	10/16/2012	10/18/2012	10/19/2012	10/21/2012
MW17	9/20/2012	9/21/2012	9/22/2012	10/1/2012
MW18	9/24/2012	9/27/2012	10/11/2012	10/12/2012
MW19	9/28/2012	9/28/2012	9/28/2012	NA (dry well)
MW20	11/6/2012	11/6/2012	11/6/2012	NA (dry well)


Notes:

TD = Total depth of drilled borehole

WELL COMPLETION DIAGRAM

MW13


Well ID:	MW13	Date Drilled:	8/11/12 - 8/18/12
Project:	Schwartzwalder Mine	Completed:	9/6/2012
Coordinates:	731263.406, 2059860.553	Developed:	9/7/12 - 9/8/12
Ground Elev.:	7401.55 ft	Static Water Lvl:	429.84 ft/btoc (10/9/2012)
Casing Elev.:	7403.00 ft	Yield Tested:	N/A
Casing Stick-up:	1.45 ft	Driller:	Layne Christenson
Casing Depth:	459.76 ft	Method:	Conventional Air
Borehole Depth:	500.76 ft	Hydrologist:	Nick Cocina, Whetstone Associates
Coordinates/datum: Colorado State Plane Central, NAD 27			

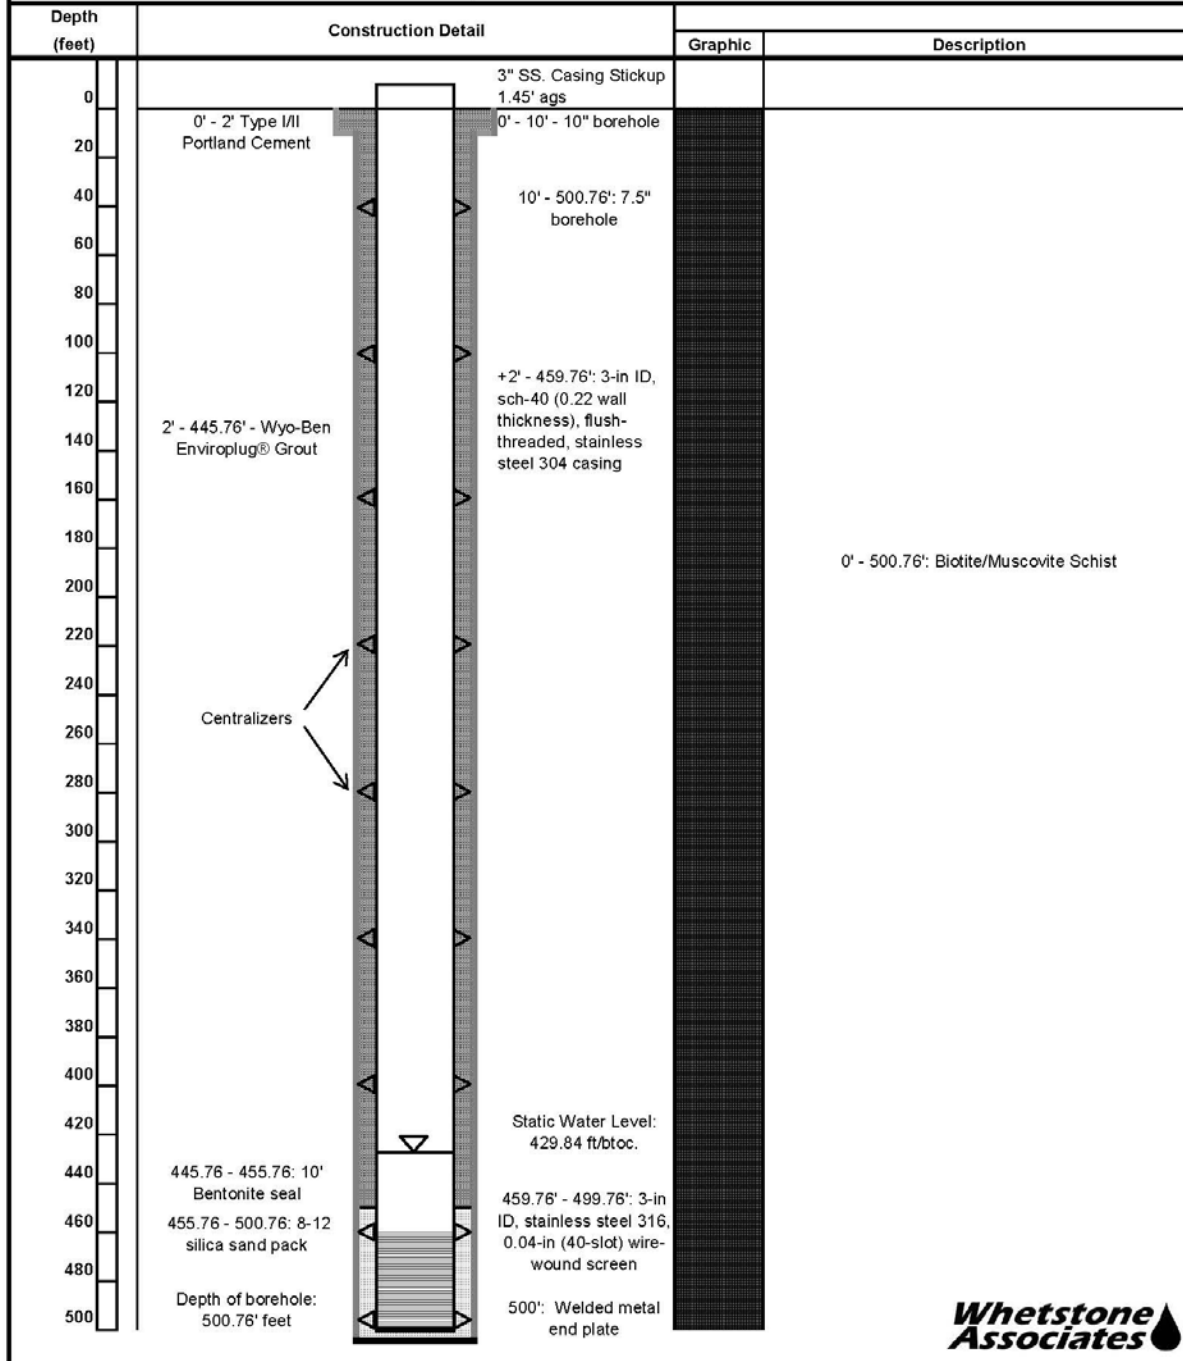


WELL COMPLETION DIAGRAM

MW14


Well ID:	MW14	Date Drilled:	8/20/12 - 8/22/12
Project:	Schwartzwalder Mine	Completed:	9/4/2012
Coordinates:	731285.116, 2059884.213	Developed:	9/14/12 -
Ground Elev.:	7401.02 ft	Static Water Lvl:	Dry
Casing Elev.:	7402.08 ft	Yield Tested:	N/A
Casing Stick-up:	0.68 ft	Driller:	Layne Christenson
Casing Depth:	134.30 ft	Method:	Conventional Air
Borehole Depth:	154.30 ft	Hydrologist:	N. Cocina, Whetstone Associates
Coordinates/datum:	Colorado State Plane Central, NAD 27		

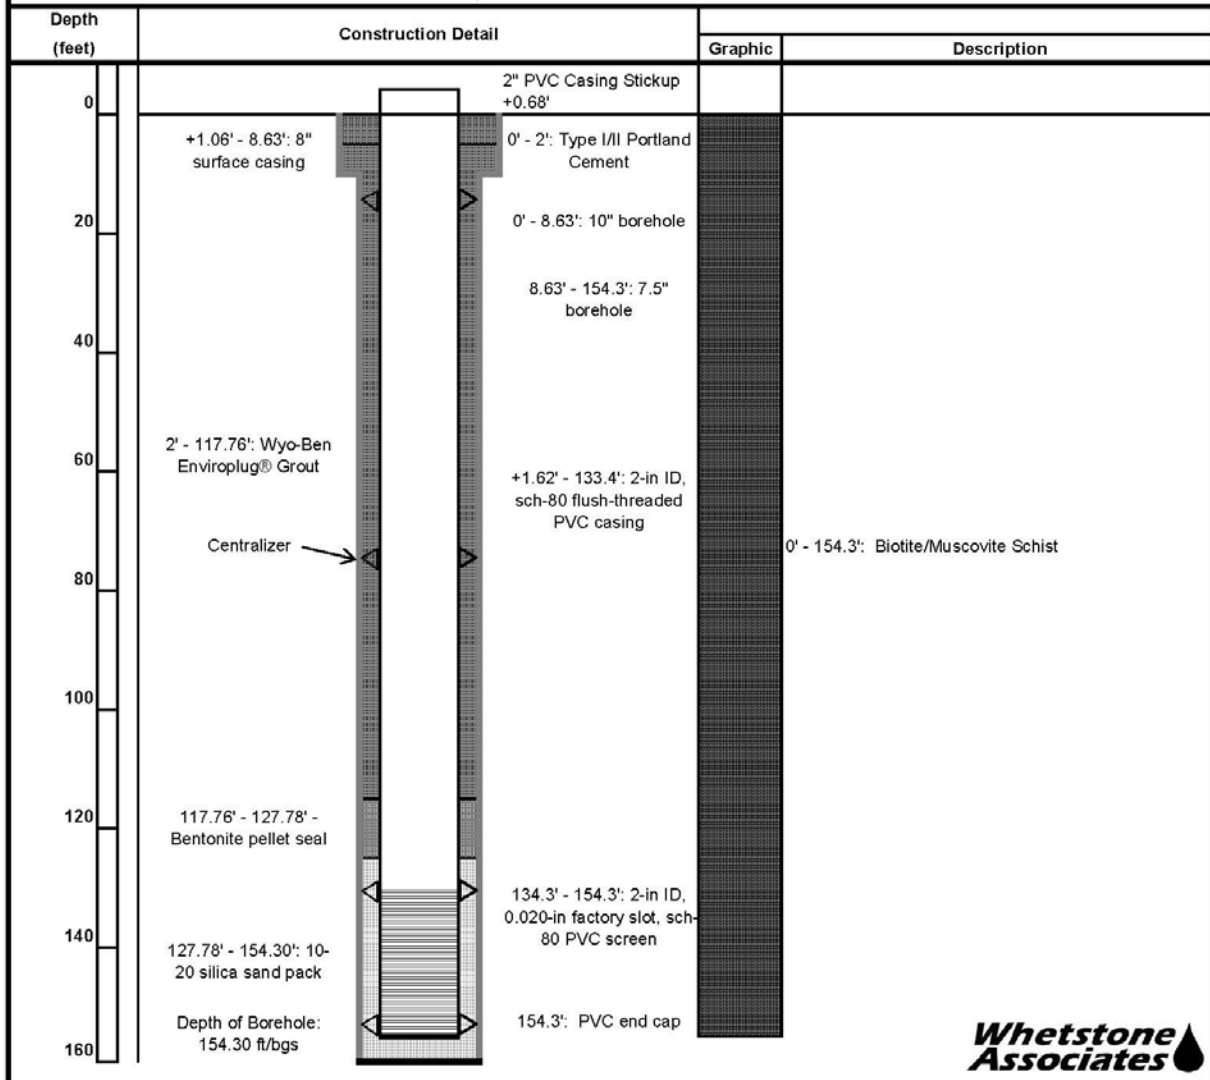

Whetstone Associates

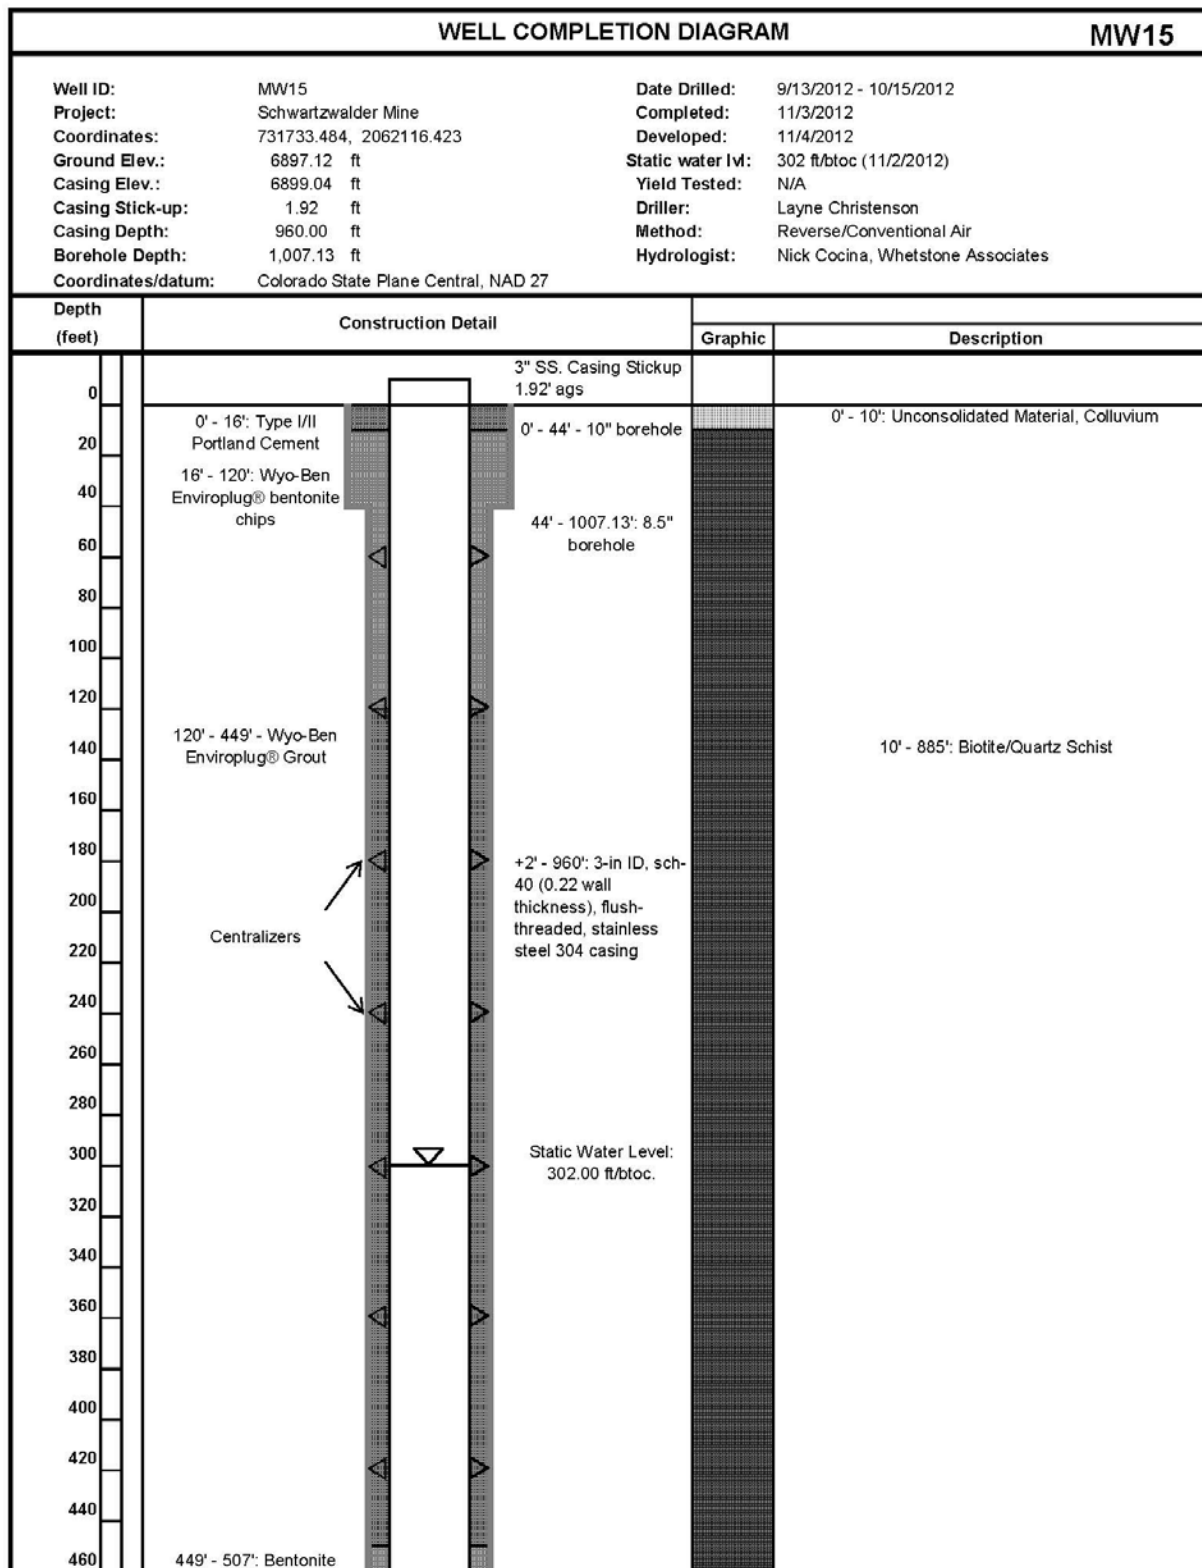

Well Completion Diagram for MW15 (upper half)

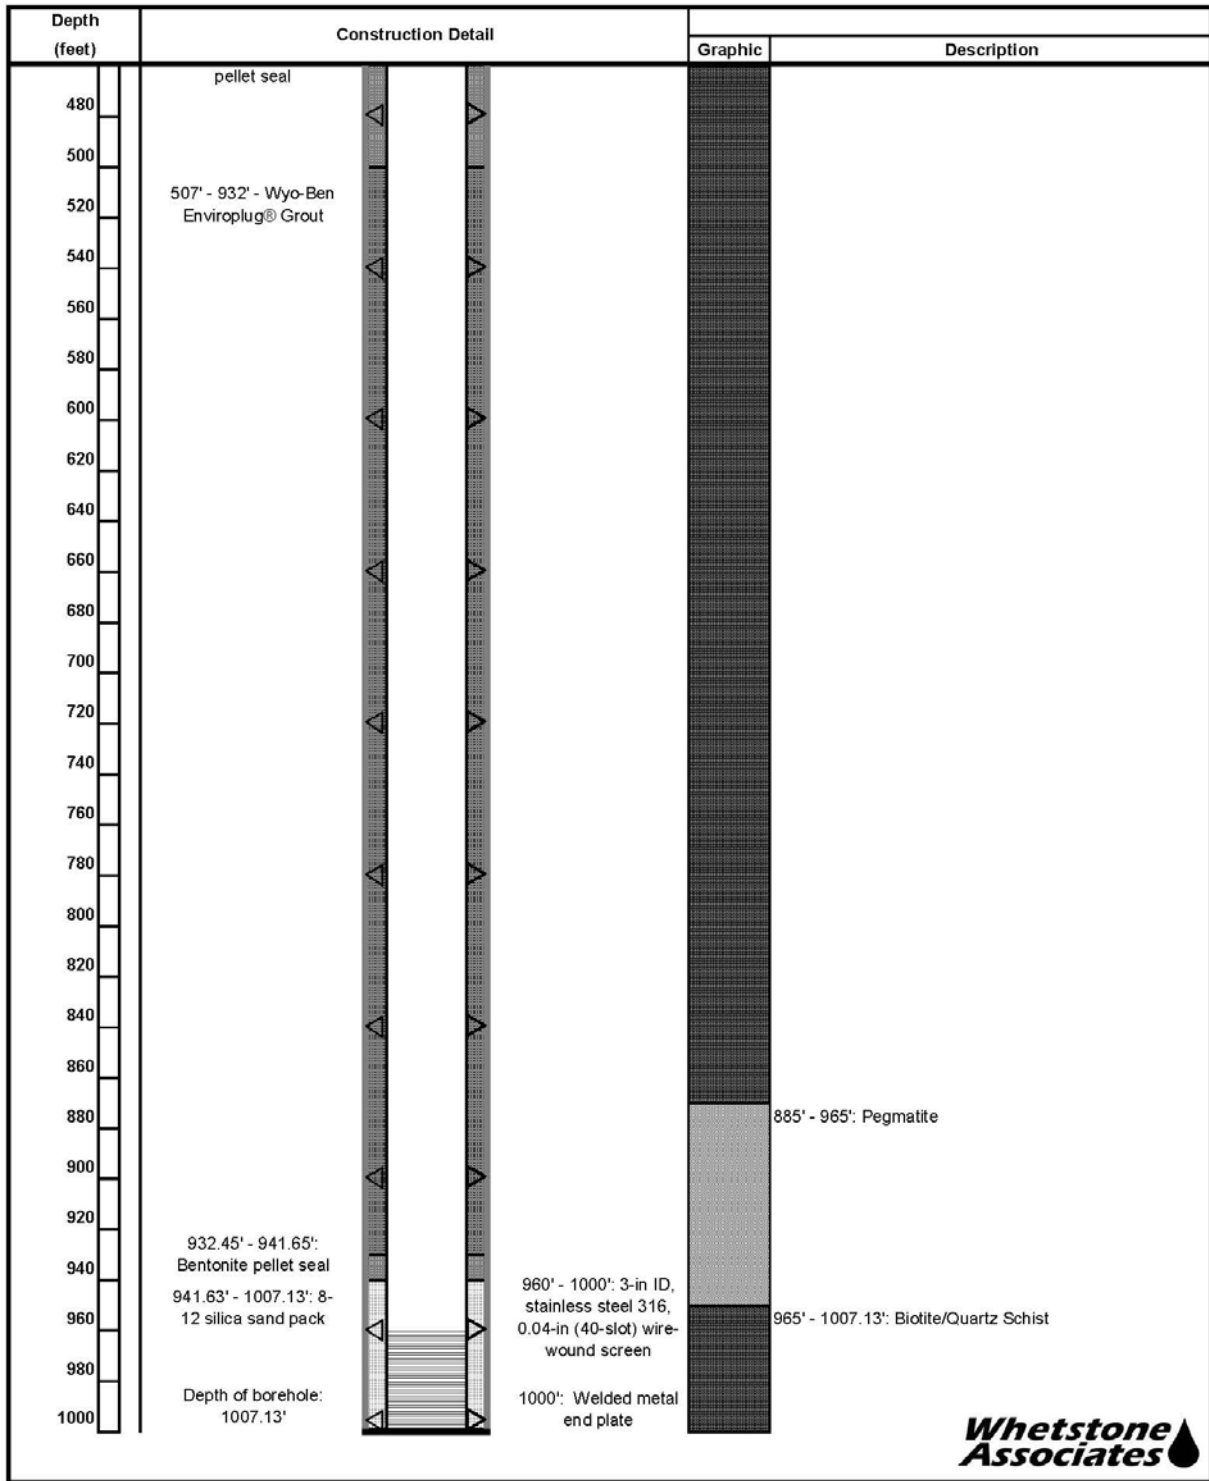


Well Completion Diagram for MW15 (lower half)

WELL COMPLETION DIAGRAM

MW16


Well ID:	MW16	Date Drilled:	10/16/2012-10/18/2012
Project:	Schwartzwalder Mine	Completed:	10/19/2012
Coordinates:	731747.714, 2062125.902	Developed:	10/20/2012 - 10/21/2012
Ground Elev.:	6898.05 ft	Static Water Lvl:	Dry
Casing Elev.:	6899.73 ft	Yield Tested:	N/A
Casing Stick-up:	1.68 ft	Driller:	Layne Christenson
Casing Depth:	300.00 ft	Method:	Reverse Air
Borehole Depth:	324.74 ft	Hydrologist:	James Haag, Whetstone Associates
Coordinates/datum:	Colorado State Plane Central, NAD 27		

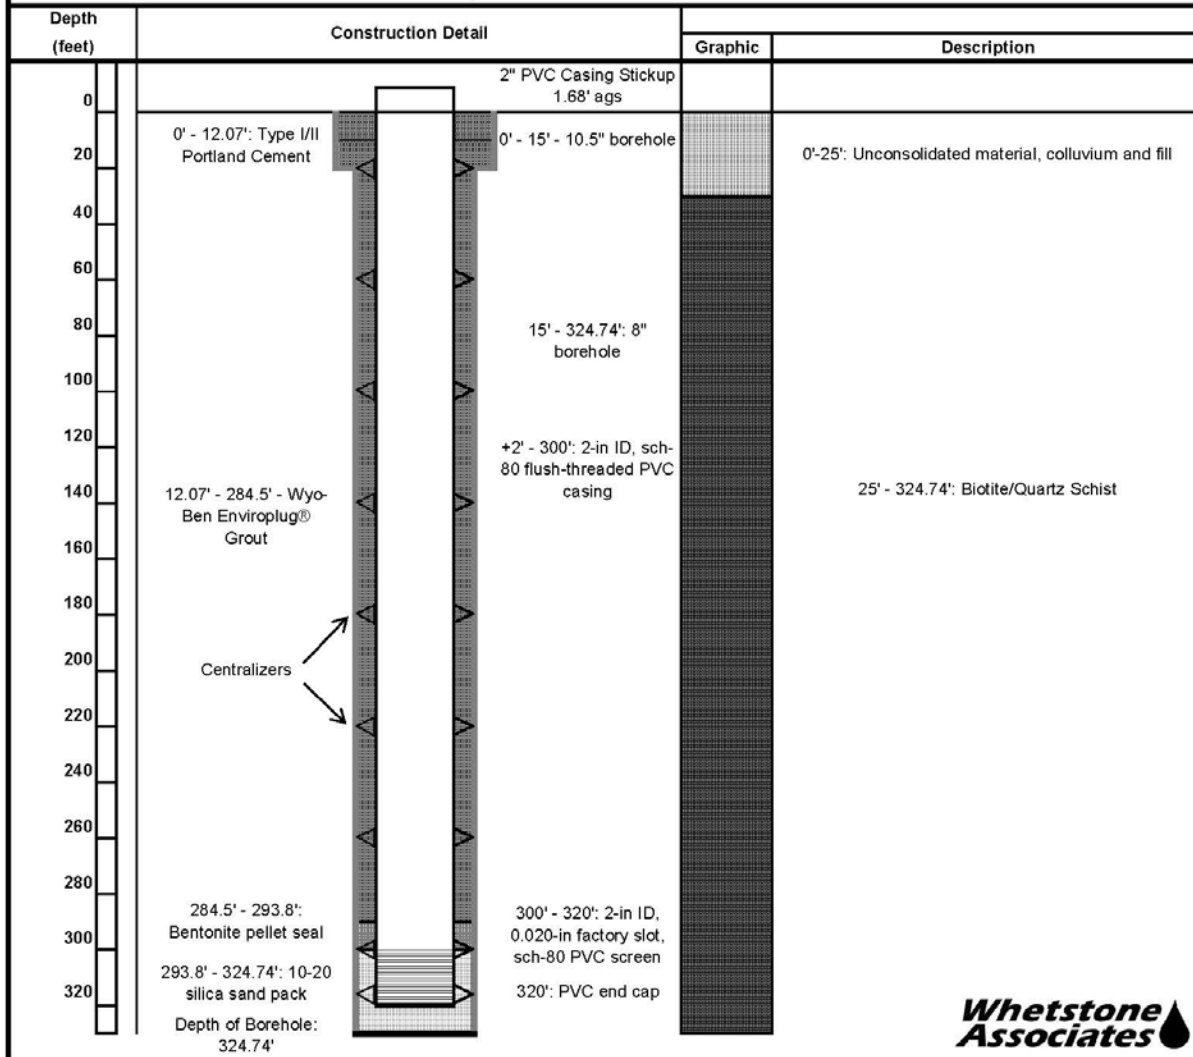

WELL COMPLETION DIAGRAM

MW17

Well ID:	MW17	Date Drilled:	9/20/2012-9/21/2012
Project:	Schwartzwalder Mine	Completed:	9/22/2012
Coordinates:	732852.317, 2061552.929	Developed:	9/23/12 - 10/1/12
Ground Elev.:	6600.34 ft	Static Water Lvl:	30.72 ft/btoc (10/9/2012)
Casing Elev.:	6601.92 ft	Yield Tested:	N/A
Casing Stick-up:	1.58 ft	Driller:	Layne Christenson
Casing Depth:	95.00 ft	Method:	Conventional Air
Borehole Depth:	119.00 ft	Hydrologist:	James Haag, Whetstone Associates
Coordinates/datum: Colorado State Plane Central, NAD 27			

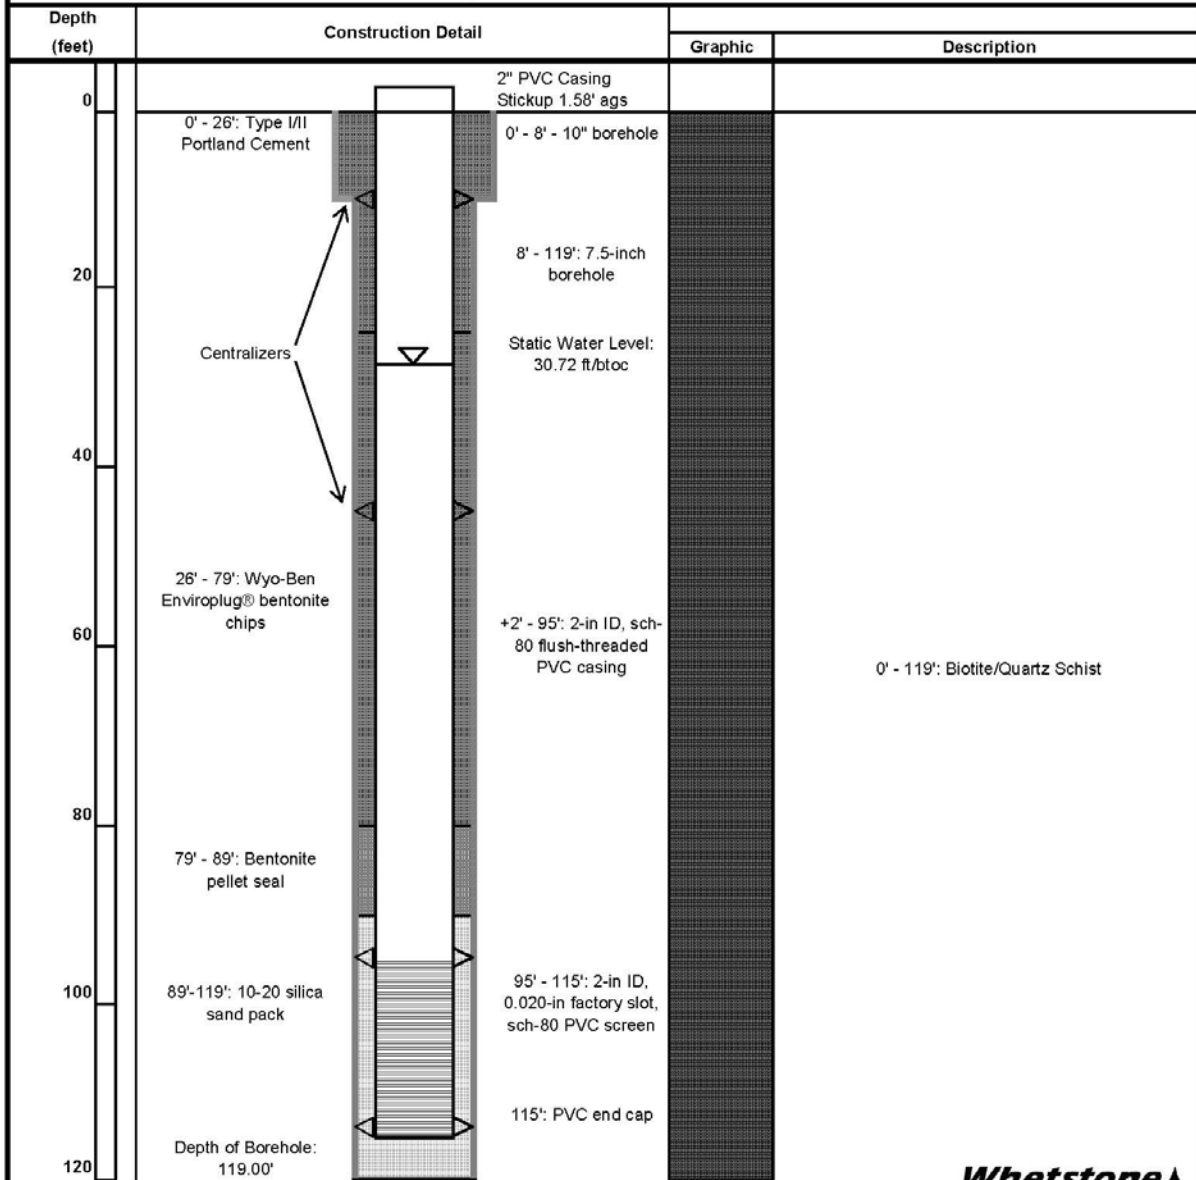


**Whetstone
Associates**

WELL COMPLETION DIAGRAM

MW18

Well ID:	MW18	Date Drilled:	9/24/12 - 9/27/12
Project:	Schwartzwalder Mine	Completed:	10/11/2012
Coordinates:	732980.675, 2061519.678	Developed:	10/12/2012
Ground Elev.:	6574.83 ft	Static Water Lvl:	4.41 ft/btoc (10/12/2012)
Casing Elev.:	6576.33 ft	Yield Tested:	N/A
Casing Stick-up:	1.50 ft	Driller:	Layne Christenson
Casing Depth:	215.00 ft	Method:	Conventional Air
Borehole Depth:	239.90 ft	Hydrologist:	James Haag, Whetstone Associates
Coordinates/datum: Colorado State Plane Central, NAD 27			

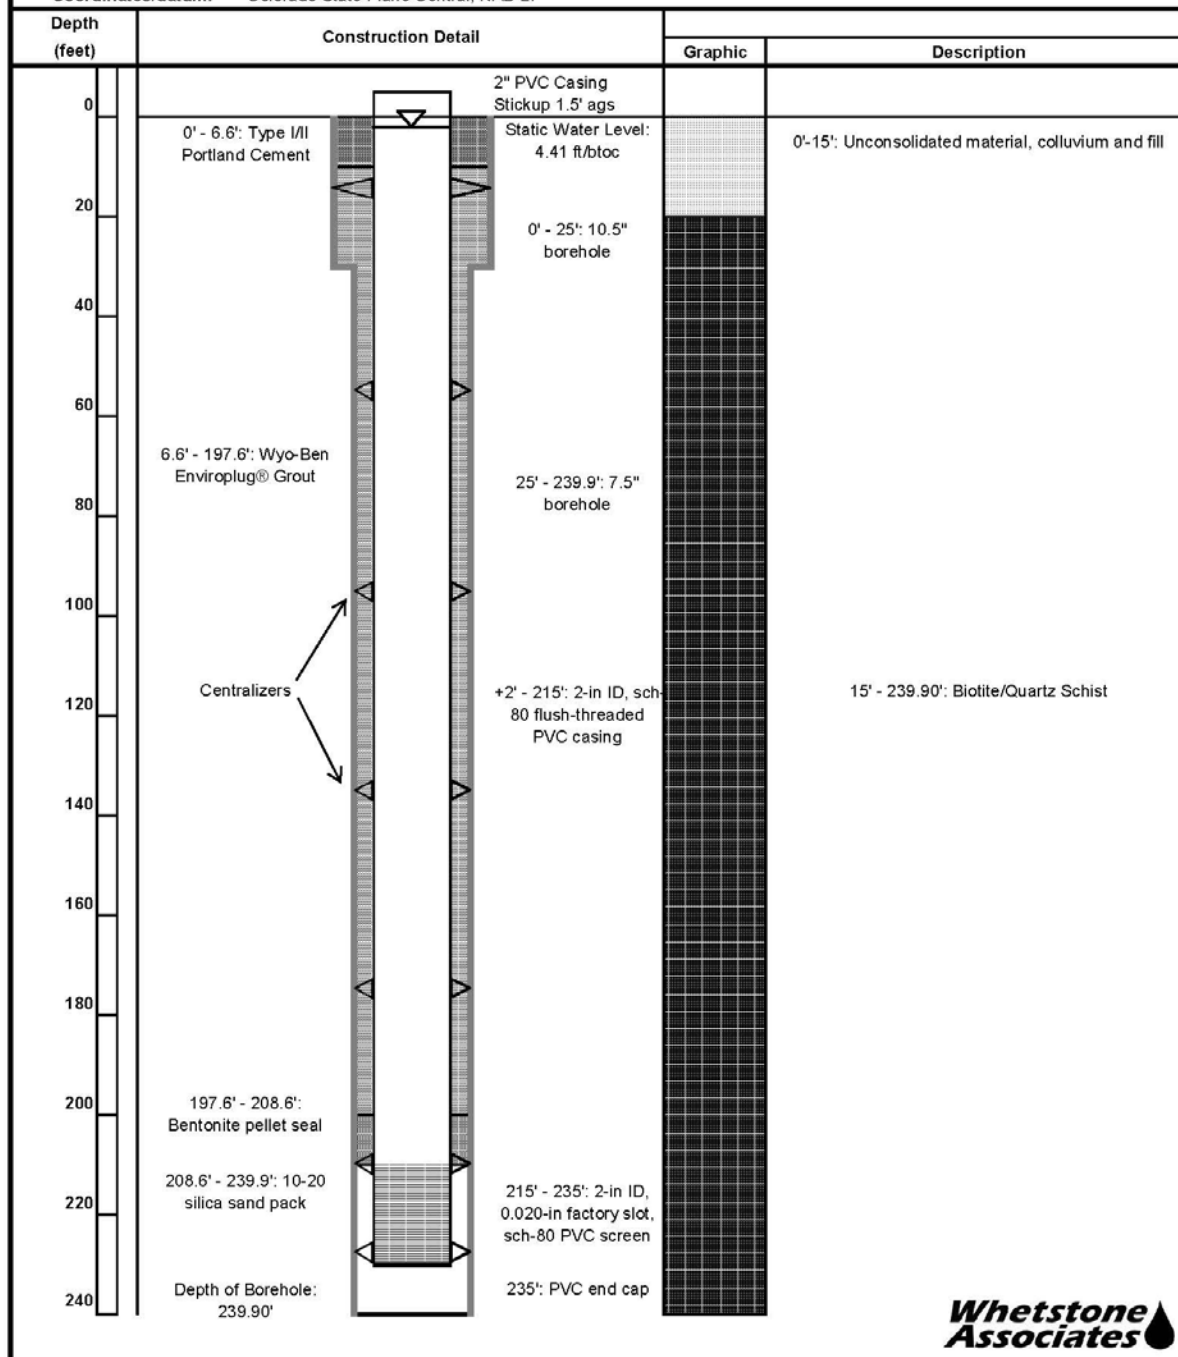


Whetstone Associates

WELL COMPLETION DIAGRAM

MW19


Well ID:	MW19	Date Drilled:	9/28/2012
Project:	Schwartzwalder Mine	Completed:	9/28/2012
Coordinates:	733571.194, 2061103.367	Developed:	NA
Ground Elev.:	6603.40 ft	Static Water Lvl:	19.73 ft/btoc (10/11/2012)
Casing Elev.:	6605.29 ft	Yield Tested:	N/A
Casing Stick-up:	1.89 ft	Driller:	Layne Christenson
Casing Depth:	10.00 ft	Method:	Reverse Air
Borehole Depth:	21.60 ft	Hydrologist:	James Haag, Whetstone Associates
Coordinates/datum:	Colorado State Plane Central, NAD 27		

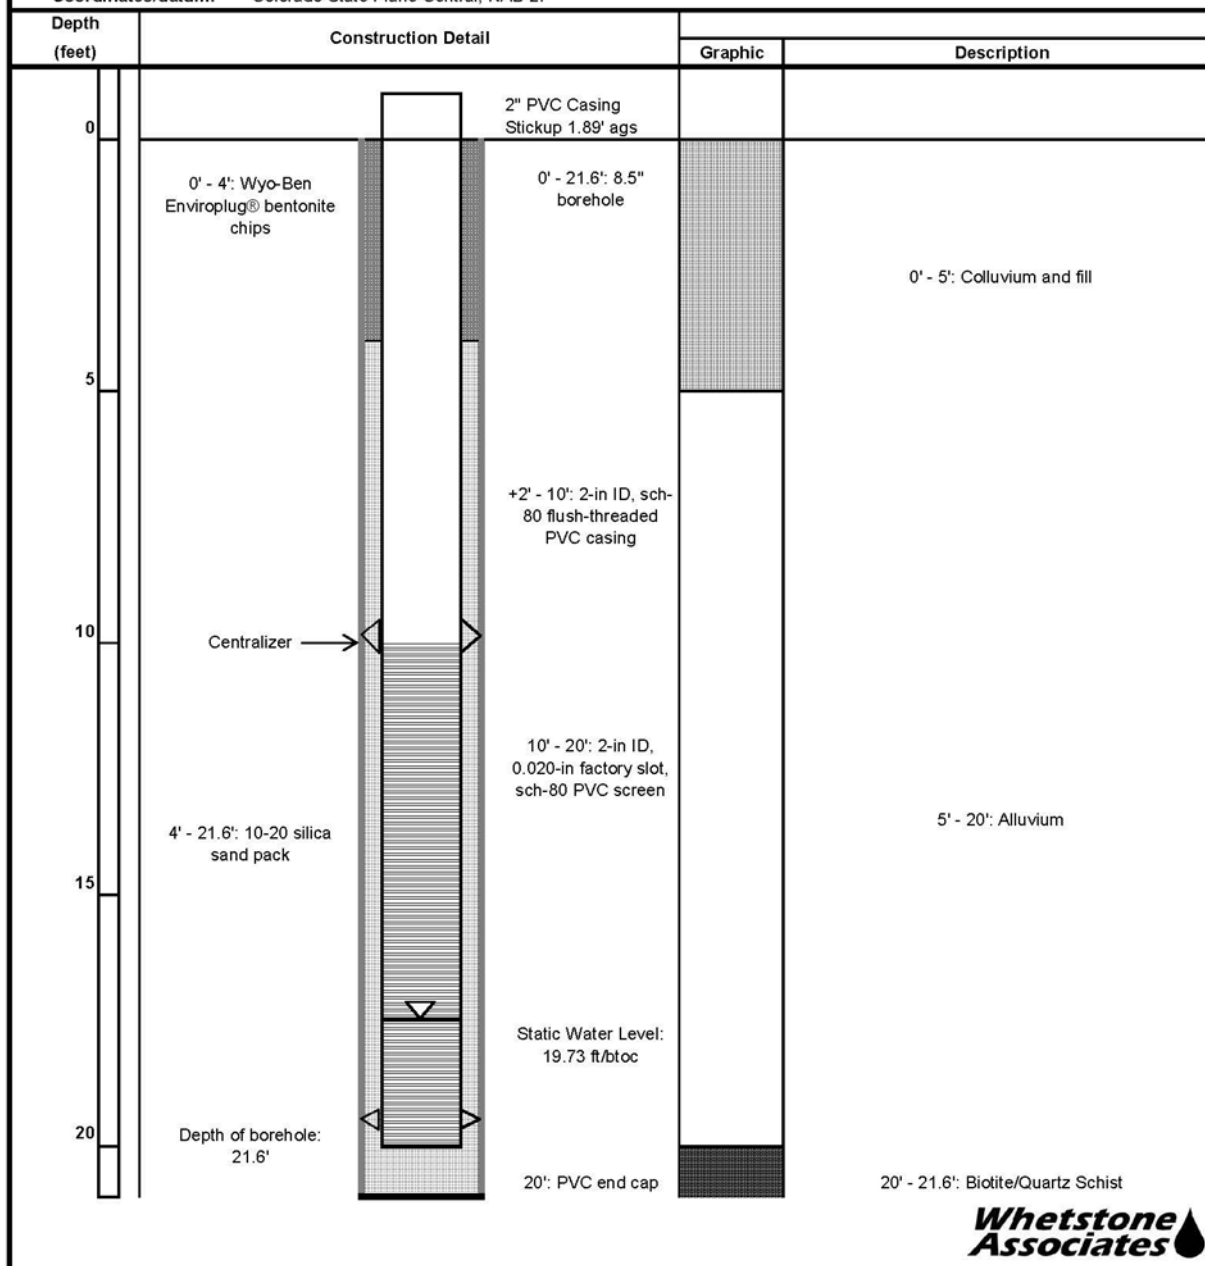

WELL COMPLETION DIAGRAM

MW20

Well ID:	MW20	Date Drilled:	9/28/2012
Project:	Schwartzwalder Mine	Completed:	11/6/2012
Coordinates:	733773.79, 2060921.156	Developed:	NA
Ground Elev.:	6644.78 ft	Static Water Lvl:	Dry
Casing Elev.:	6646.72 ft	Yield Tested:	N/A
Casing Stick-up:	1.94 ft	Driller:	Layne Christenson
Casing Depth:	40.00 ft	Method:	Reverse Air
Borehole Depth:	50.00 ft	Hydrologist:	James Haag, Whetstone Associates
Coordinates/datum:	Colorado State Plane Central, NAD 27		

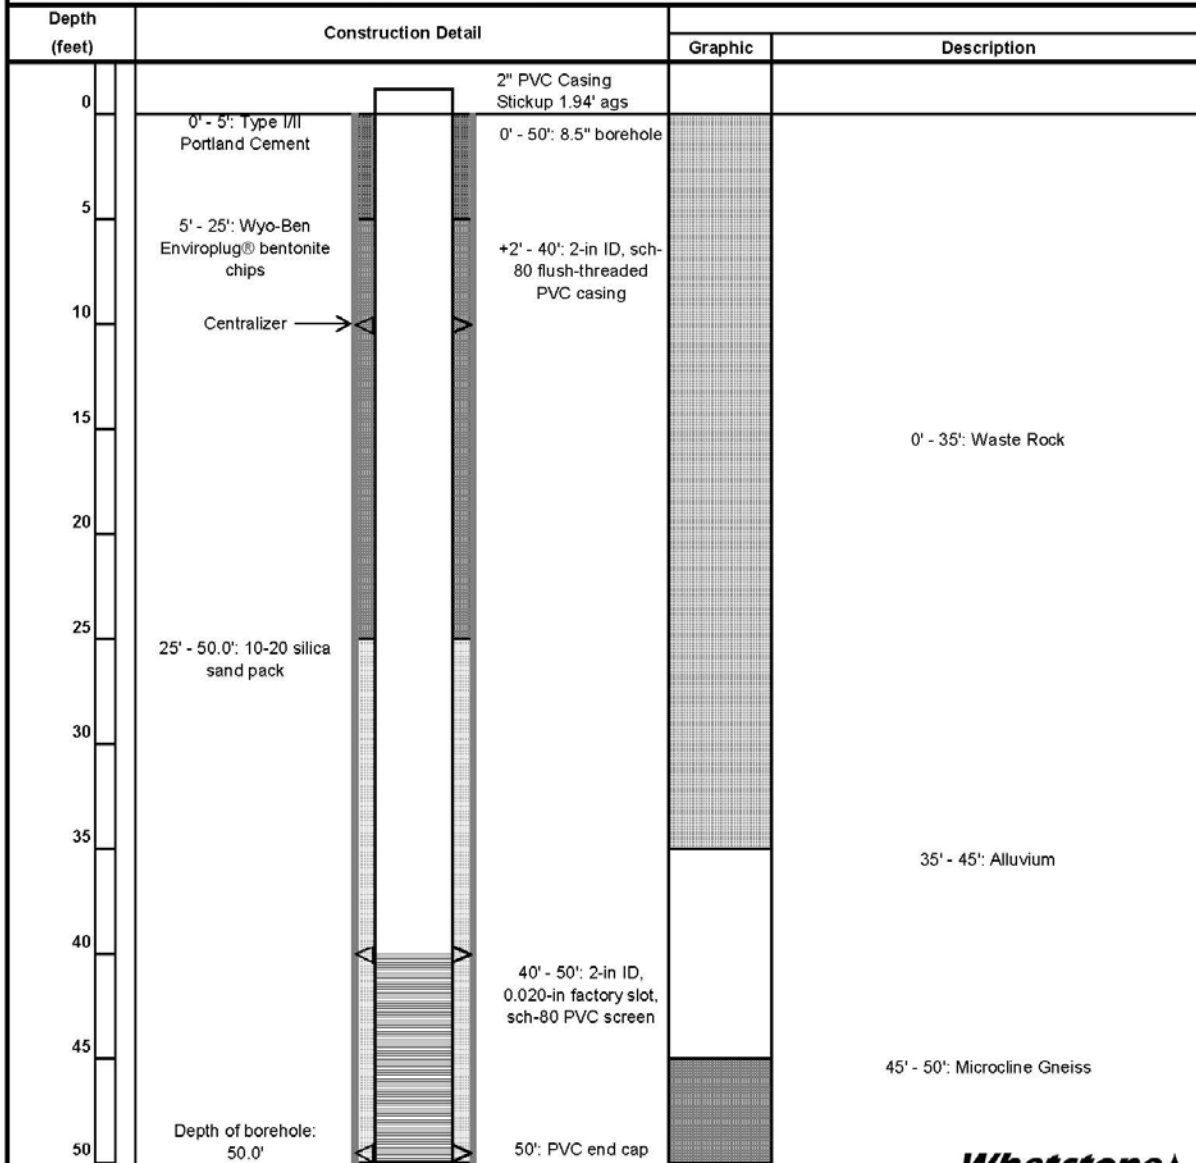

Whetstone Associates
