

to delineate the permit boundary (see Photo 5).

<u>Permit Stipulations:</u> There is a commitment to request an increase to the financial warranty prior to opening the "South Pit".

<u>Storm Water MGT Plan:</u> No oil or fuel spills observed. Ditches (see **Photo 6**) were observed intended to divert runoff away from the pit and towards a stormwater pond on the southwest corner of the existing pit. Stormwater captured within the pit, infiltrates.

Topsoil: A topsoil stockpile was observed on the north side of the existing pit (see Photo 7).

Please contact Tim Cazier (303)866-3567 ext. 8169 or email at  $\underline{\text{tim.cazier@state.co.us}}$  if you have any questions regarding this report.

### **PHOTOGRAPHS**



Photo 1. East (center background) and west (foreground) highwalls sloped at 5H:1V or flatter (looking NE).

## **PHOTOGRAPHS** (cont.)

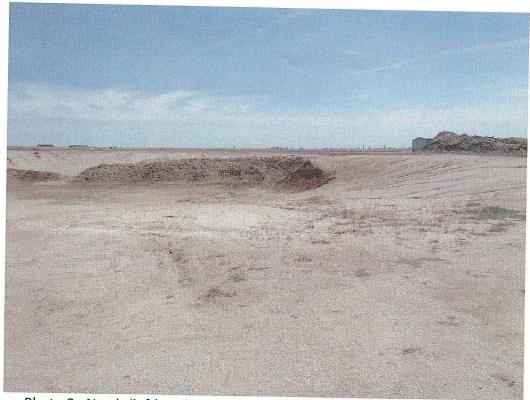


Photo 2. North (left) and west (right) highwalls sloped at 3H:1V or flatter.

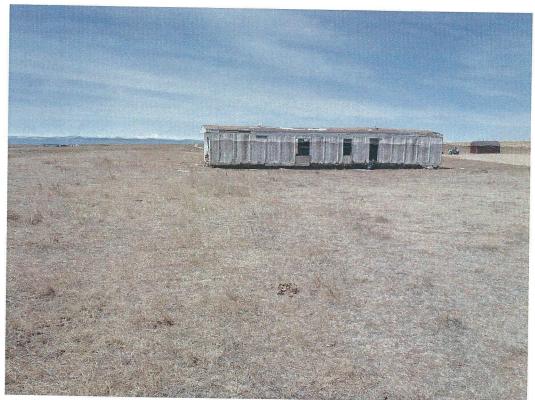


Photo 3. House trailer in poor condition within permit boundary (south side, looking west).

# **PHOTOGRAPHS** (cont.)



Photo 4. Permit sign (at gated entrance, looking east).



Photo 5. Typical permit boundary marker (SE corner, looking north).

### **PHOTOGRAPHS** (cont.)



Photo 6. West side diversion ditch (looking north).



Photo 7. North pit topsoil stockpiles (north side, looking west).

PERMIT #: M-2008-025 INSPECTOR'S INITIALS: TC1 INSPECTION DATE: April 10, 2018

### **Inspection Contact Address**

Tim Kunau 23945 Lucky Lane Calhan, CO 80808

ec: DRMS file
