

ADDENDUM 1

Sunrise Metals Inc. - REX Exploration Project – 2023 Annual Report

Drill Hole	E NAD83	N NAD83	Depth (ft)	Angle	Start	End
REX-01	698927	4246334	270	-90	7/1/2023	7/10/2023
REX-02	698889	4246299	335	-90	7/10/2023	7/22/2023
REX-03	698976	4246318	150	-90	7/23/2023	7/26/2023
Lay-Down	699296	4246954	0		not used	not used
Mud Pits:						
REX-01	5 yards, north of collar site for REX-01; pit was back filled					
REX-02	4 yards, north of collar site for REX-02; pit was back filled					
REX-03	Drill water for REX-03 was conveyed by 3-inch flex hose to mud pit at REX-01					
No excavation, rock dumps, adits, trenches or pits were constructed.						

The main access road has been in existence since prior to 1952. Intermittent sections of that trail were accomplished to facilitate travel and safety issues. Side road channels and water bars were created locally to improve drainage conditions.

Figure 1: Location map of the areas of 2023 activities.

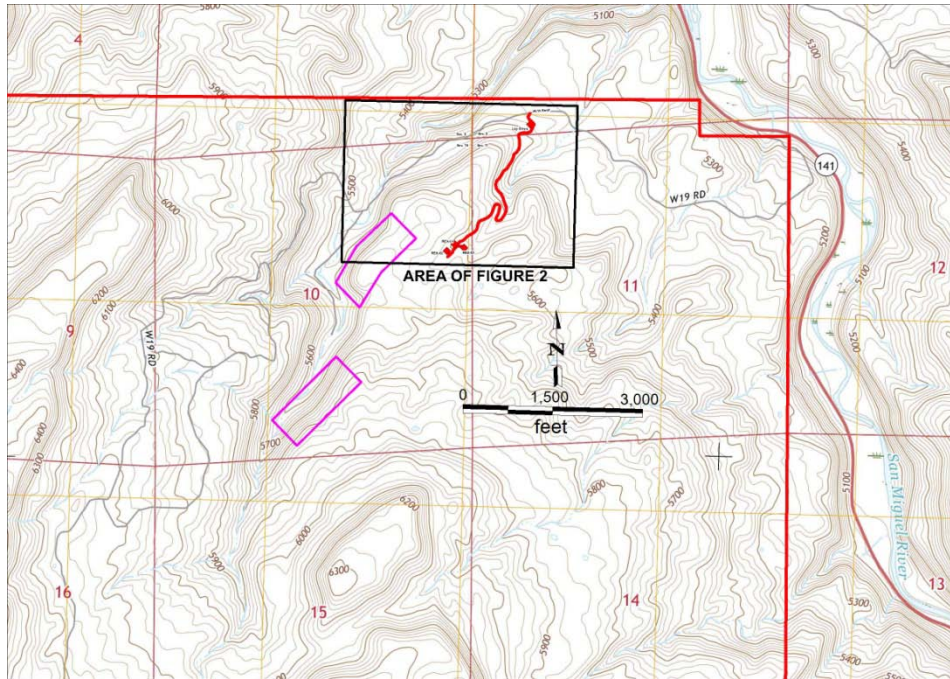


Figure 2: Map of 2023 drill sites and access road showing areas of intermittent upgrades.

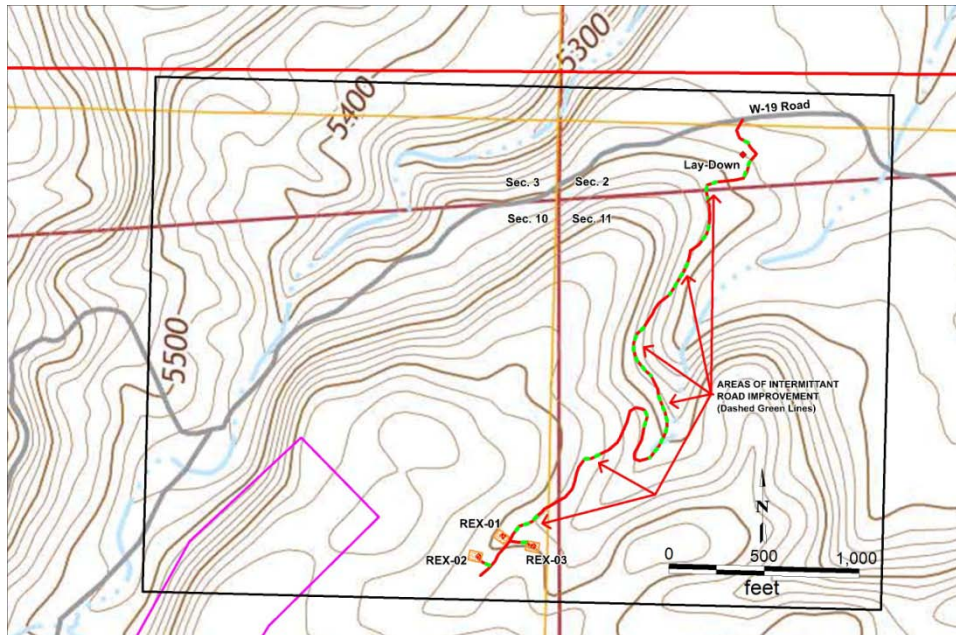


Figure 3: Drone image of REX-01 drill site after scarification and implementation of storm water control measures.



Figure 4: Drone image of drill site REX-02 after scarification and implementation of storm water control measures.



Figure 5: Drone image of drill site REX-03 showing storm water control measures.

