



Schwartzwalder Daily Summary Report

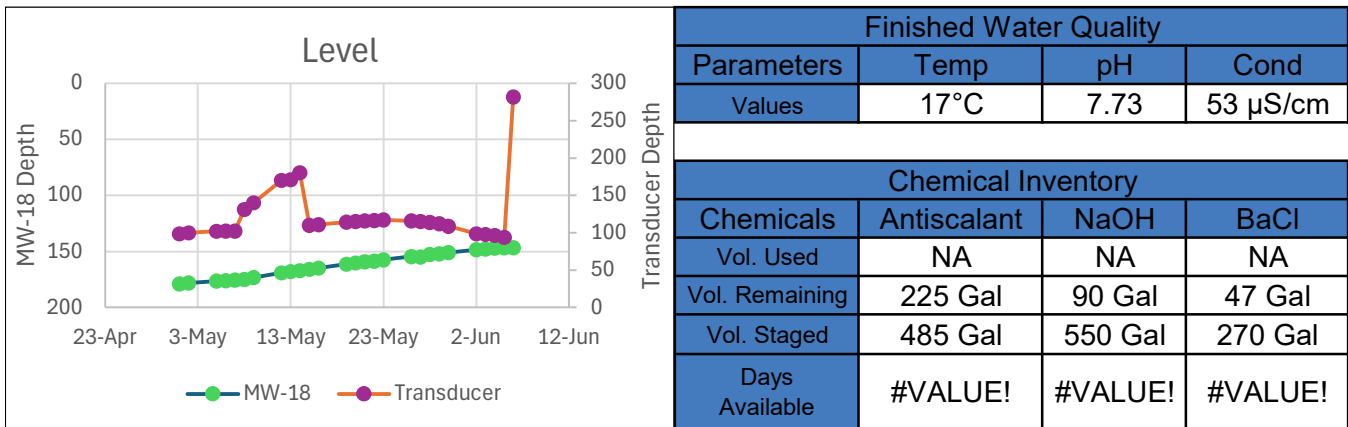

Report Date:	6/6/2025	Lead Operator:	Patrick D
		Assistant Operator(s):	Bryant A Alex S

Effluent Discharged:	0.000 Mgal	MW-18 Level:	147 ft
Average Flowrate:	0 gpm	Transducer Level:	282 ft
Effluent to Date:	0.000 Mgal		

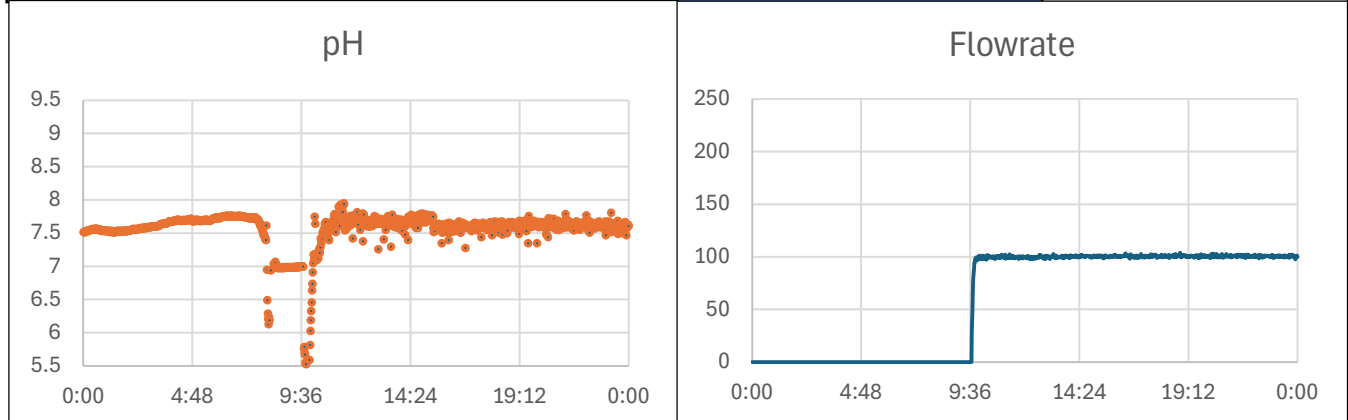

Safety Issues/Concerns:
 - N/A

Notes:
 - Patrick Delaney and Matt Collins / Black Fox Mining onsite.
 - Alex Schwieber / Linkan Engineering onsite.
 - 700 ft DRMS Transducer is stuck.
 - Item B38 Completed. Installed 600' Mine Pool Transducer and Cable.
 Note: The New transducer is a longer depth so it will read more head pressure , therefore the Level Graph will spike.



Schwartzwalder Daily Summary Report 6/6/25

1 message

Bryant Acevedo <bryant.acevedo@linkan.com>

Fri, Jun 6, 2025 at 3:44 PM

To: Peter Hays - DNR <peter.hays@state.co.us>

Cc: Adam Billin <Adam.Billin@linkan.com>, Sam Billin <sam.billin@linkan.com>, Quinn Westmoreland <quinn.westmoreland@linkan.com>, Brandy Wadford <brandy.wadford@linkan.com>, Jared Buck <jared.buck@linkan.com>, Alex Schwiebert <alex.schwiebert@linkan.com>, Chris Prosper <chris.prosper@linkan.com>, Patrick Delaney <pdelaney@blackfoxmining.com>

Good afternoon,

See attached for today's summary report and pictures of the Transducer work completed today / Item B38.

Best,

Bryant Acevedo
Operator Technician



cell: 720-238-6169

linkan.com • bryant.acevedo@linkan.com

PLEASE NOTE: This message, including any attachments, may include privileged, confidential and/or inside information. Any distribution or use of this communication by anyone other than the intended recipient is strictly prohibited and may be unlawful. If you are not the intended recipient, please notify the sender by replying to this message and then delete it from your system.

7 attachments



IMG_8099.jpeg
928K




IMG_8100.jpeg
1170K



IMG_8101.jpeg
1088K



IMG_8105.jpeg
1319K

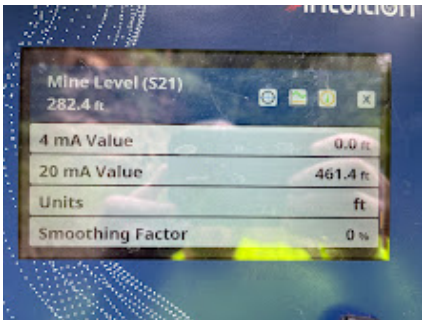

IMG_8106.jpeg
911K

 **SWTP Daily Summary Report 6.6.25.pdf**
235K

 **IMG_8103.mov**
1573K











Mine Level (S21)

282.4 ft



4 mA Value

0.0 ft

20 mA Value

461.4 ft

Units

ft

Smoothing Factor

0 %
