



TR-133 WHEX Clay Borrow Source - Final Figures

Johnna Gonzalez <Johnna.Gonzalez@newmont.com>

Mon, Feb 6, 2023 at 1:39 PM

To: "Russell - DNR, Elliott" <elliott.russell@state.co.us>

Cc: Katie Blake <Katie.Blake@newmont.com>, Norma Townley <Norma.Townley2@newmont.com>

Hi Elliott,

I submitted TR-133 regarding the WHEX Clay Borrow Source through the DRMS website on 2/3/2023. In looking at the submittal, I noticed the figures still have "DRAFT" on them. Could you please replace the draft figures with the attached final figures. If you have any questions or concerns, please let me know.

Thanks,



Johnna Gonzalez

ENVIRONMENTAL

100 N 3rd Street
PO Box 191

Victor, CO 80860

M 719.313.0447

NEWMONT.COM

2 attachments



WHEX Clay Excavation Closure Figure.pdf


777K





WHEX Clay Excavation Figure - Revised Slopes.pdf

675K

P:\Projects\0106.056 VLF2 Phase 3a COA\A-CAD\FIGS\0106.056.071F.dwg-2/6/2023 12:22 PM

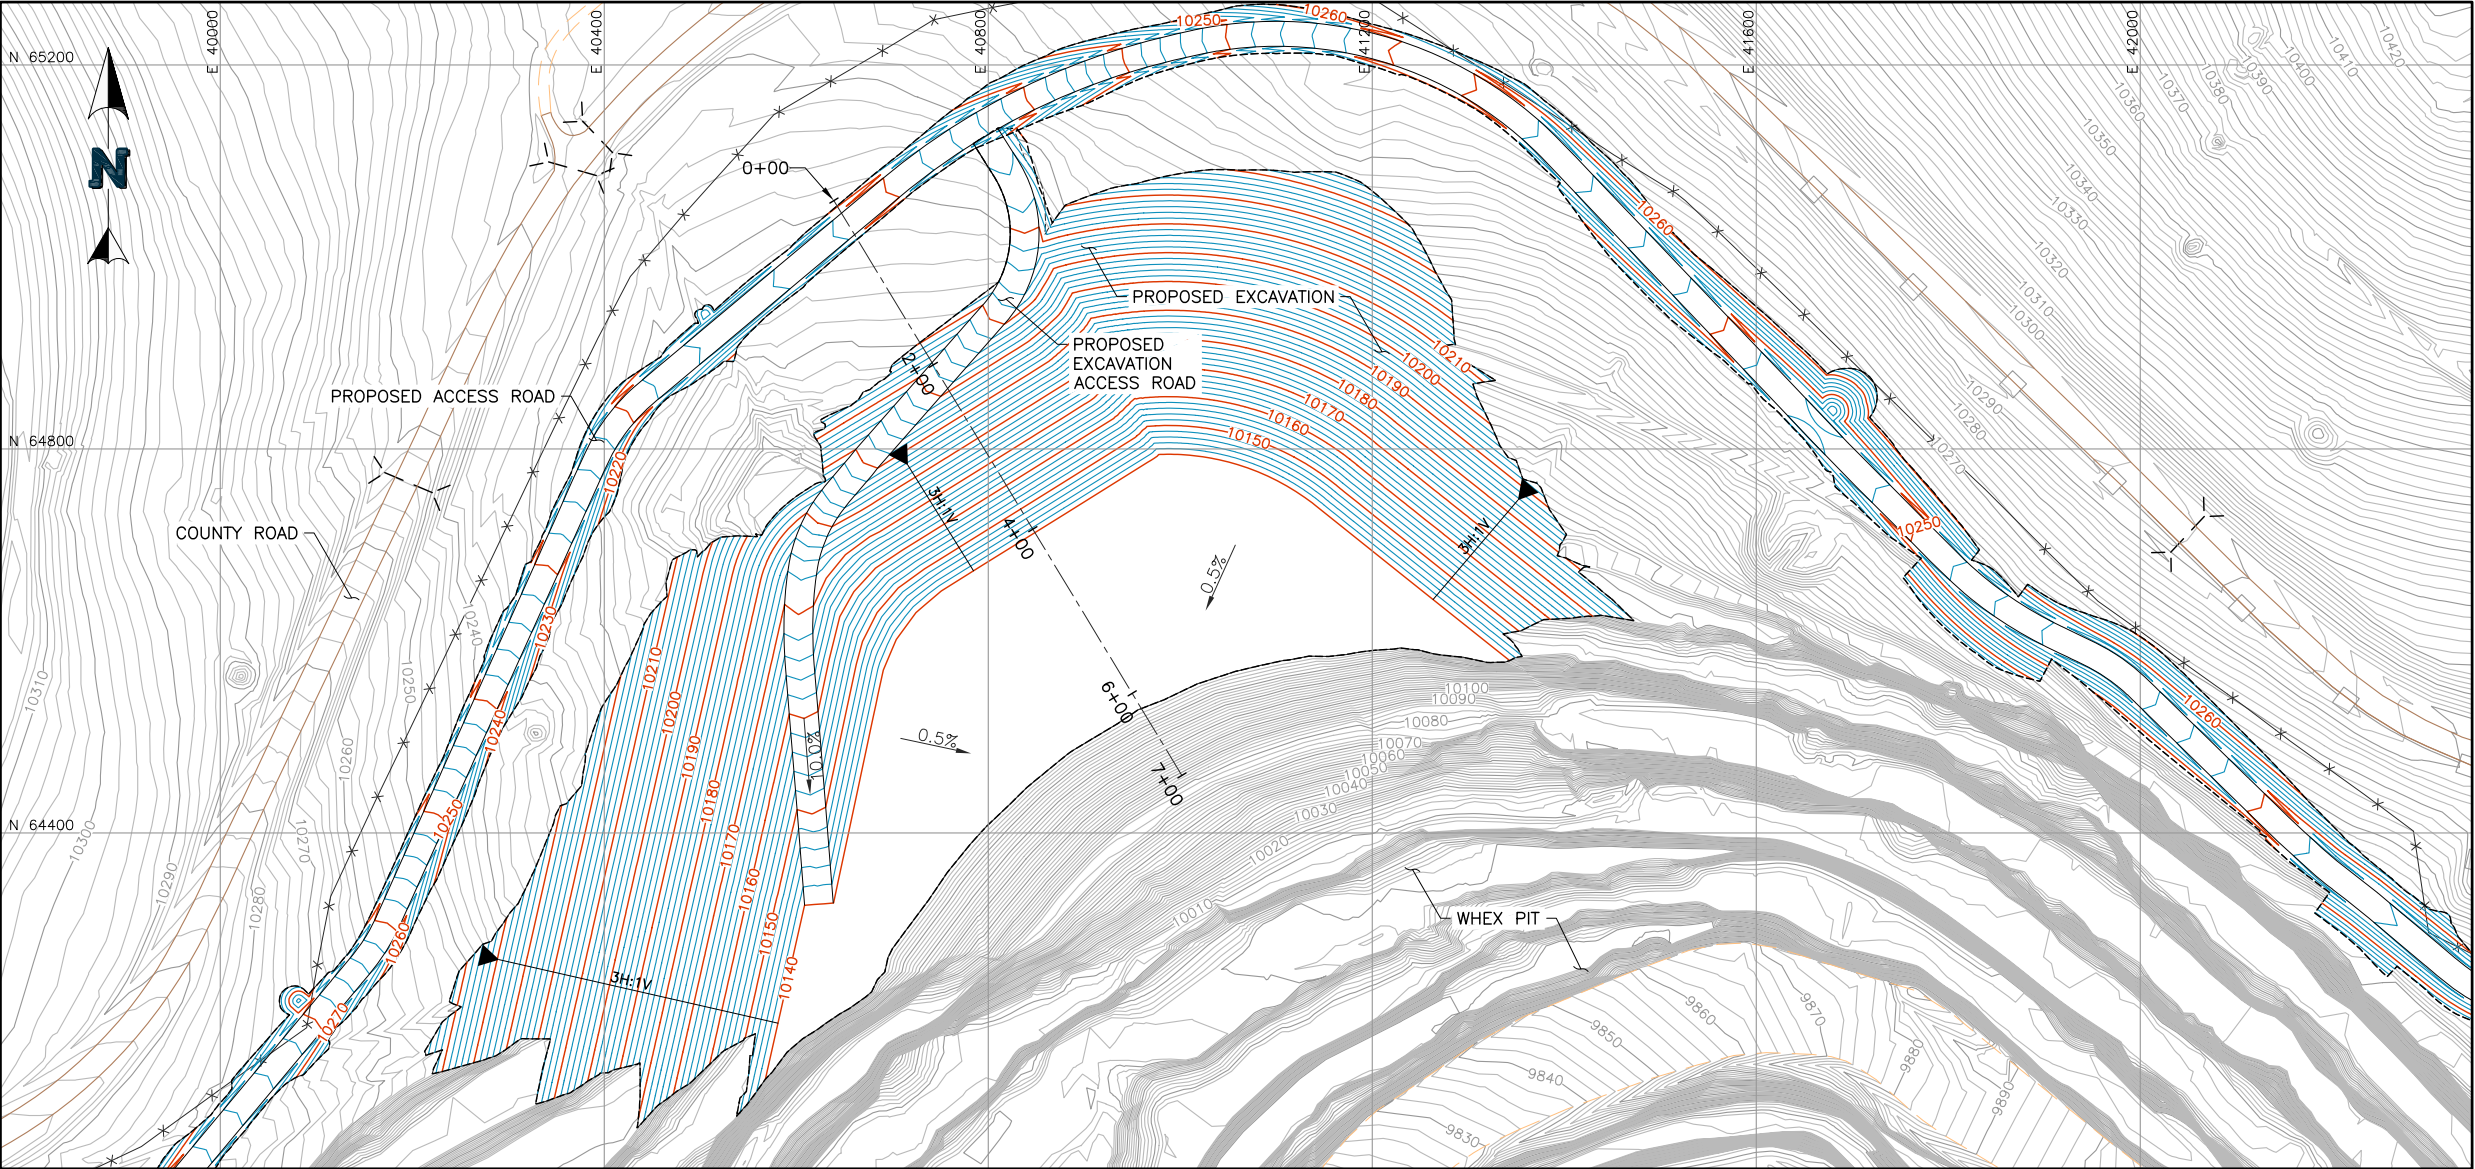


- LEGEND:**
- EXISTING GROUND CONTOURS
 - PROPOSED GROUND CONTOURS
 - EXISTING ROADS/TRAILS
 - EXISTING FENCE
 - EXISTING CULVERT

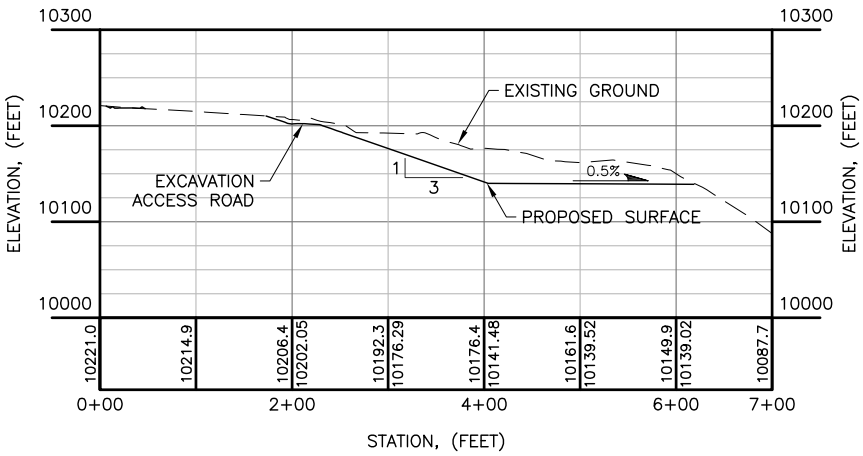

		CLIENT	CRIPPLE CREEK & VICTOR GOLD MINING COMPANY		
PROJECT		VLF2 PHASE 3			
TITLE		WHEX PIT CLAY EXCAVATION - 10140'		FILENAME 0106.056.071F	
				FIGURE NO. 1	REVISION A

P:\Projects\0106.056 VLF2 Phase 3a CQA\A-CAD\FIGS\0106.056.078F.dwg-1/10/2023 4:21 PM

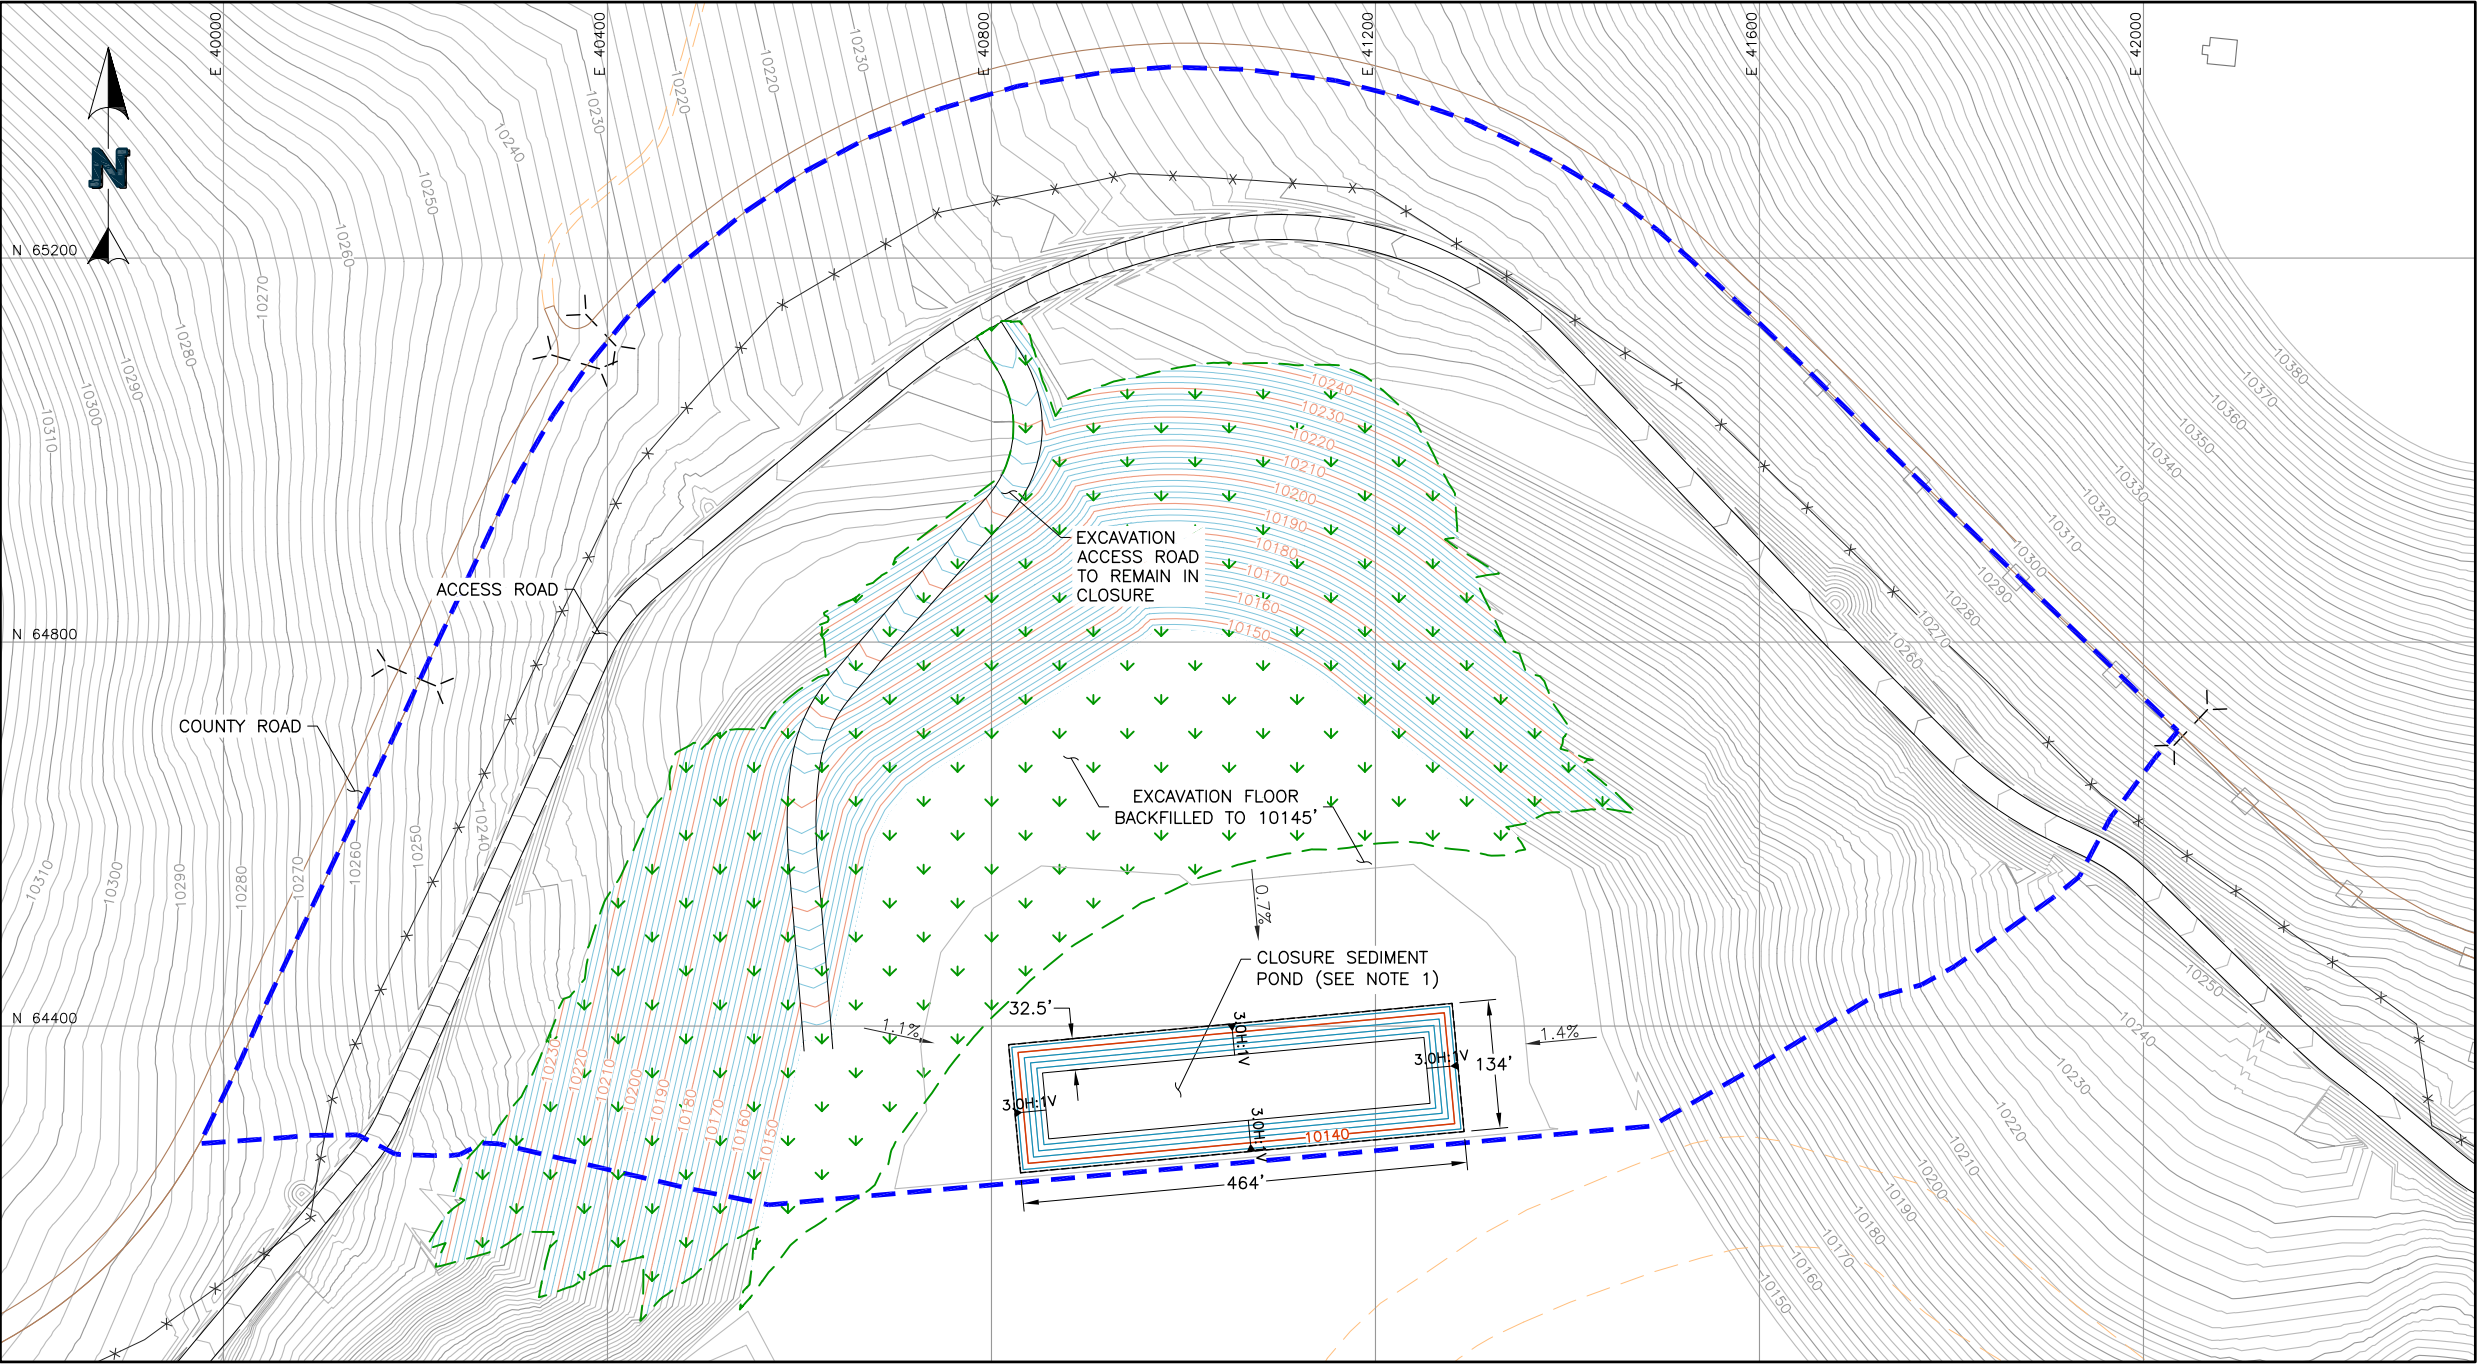

- LEGEND:**
- CLOSURE CONTOURS
 - POND CONTOURS
 - EXCAVATION CONTOURS
 - EXISTING ROADS/TRAILS
 - EXISTING FENCE
 - WATERSHED BOUNDARY
 - DISTURBANCE BOUNDARY
 - EXISTING CULVERT

- NOTES:**
- CLOSURE SEDIMENT POND VOLUME AT FREEBOARD ELEVATION (10141') IS 358,880 ft³.
 - TOTAL RUNOFF VOLUME FOR 500 YR, 24 HR DESIGN STORM IS 357,610 ft³.
 - APPROXIMATELY 20,753 yd³ OF TOPSOIL REQUIRED FOR 12" DEPTH.

NewFields		CLIENT CRIPPLE CREEK & VICTOR GOLD MINING COMPANY	
PROJECT		VLF2 PHASE 3	
TITLE		FILENAME	
WHEX PIT CLAY EXCAVATION RECLAMATION		0106.056.078F	
		FIGURE NO.	REVISION
		2	A
