RECLAMATION KEY

- PROPERTY / PERMIT / LEASE BOUNDAR
- MINING AREAS
- DOZER RECLAMATION
- SCRAPER RECLAMATION
- COMPLETED SLOPE WORK
- CONCRETE IMPORT RECLAMATION

ESTIMATED RECLAMATION SCHEDULE

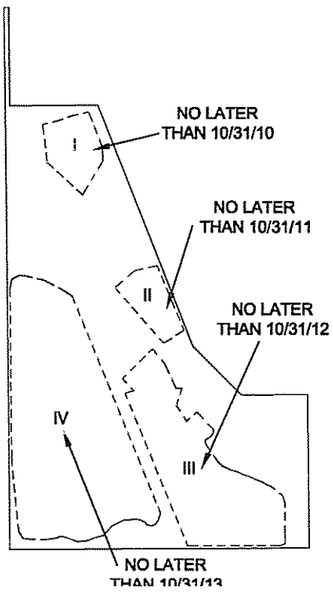

NOTE:
RECLAMATION SHALL MEAN ANY GRADING AND SEEDING REQUIRED BY COLORADO DRMS PERMIT.

RECLAMATION COMPLETION DATES ARE ESTIMATES AND DEPEND UPON MARKET CONDITIONS, BUT NONETHELESS SHALL BE COMPLETED IN ACCORDANCE WITH THE TIMELINE SET FORTH IN PARAGRAPHS 5.J AND 5.K OF THE LEASE.

SCALE HOUSE

(MINING COMPLETE)

DOZER RECLAMATION

OVERBURDEN STOCKPILE AREA 8 AC.

100 FT. POWERLINE EASEMENT

TO REMAIN IN PLACE

OB STOCKPILE AREA 4 AC.

DISTURBED AREA OUTSIDE CELLS 1 & 2 TO BE RECLAIMED PER DRMS PLAN

(MINING COMPLETE)

DOZER RECLAMATION

CURRENT MINING PHASE

OB=100,000 CY TO REMAIN IN PLACE

CONCRETE IMPORT 93,750 CY

EXISTING RECONFIGURED SLOPES TO REMAIN IF AT LEAST 2H:1V TYP. AREA

SLOPE WORK COMPLETED

PARTIAL TOPSOIL FINAL GRADING TO COMPLETE

MINING PHASE 2

WATERLINE

WATERLINE EASEMENT

WATER LINE EASEMENT TO BE VACATED BY THE CITY OF FOUNTAIN REMAINING MATERIAL TO BE REMOVED TO CREATE ONE CELL

WATER LINE WITHIN CELL TO BE REMOVED BY LAFARGE (NO SOONER THAN 11/01/2010)

(MINING COMPLETE, RECLAMATION ONGOING)

SCRAPER RECLAMATION

100 FT. POWERLINE EASEMENT

MINING PHASE 3

(MINING COMPLETE)

SLOPES CONSTRUCTED DURING LEASE PERIOD WILL BE 2H:1V TYP. AREA

RESERVOIR CELL 2

SCRAPER RECLAMATION

DOZER RECLAMATION

SETTLING PONDS TO REMAIN

SCRAPER RECLAMATION

DOZER RECLAMATION

RESERVOIR CELL 1

N W E S

EXHIBIT B

LAFARGE AGGREGATES & CONCRETE

10170 CHURCH RANCH BLVD, SUITE 200 – WESTMINSTER, CO. 80021 303.657.4000

PROJECT:	FOUNTAIN
TITLE:	RECLAMATION PLAN
DRAWN BY: ROR	DATE: 01/05/2010 SCALE: 1"=300'
FILE PATH:	SHEET NO.

K:\Projects\001003 - Fountain\Art\Mine Plan\2008 Mine Plan\2008 Rework Drawings\Fountain 2008 Rework.dwg, RECLAMATION, 1/5/2010 9:21:58 AM
